R/c

J.N.& Co.
FROM CONCEPT TO CREATION

Ref # JN/Engg/Site/ECP/285

Date: 04/03/2026

RECEIVED
Date 06-March-2026
Time 11:30 am
CGD Consulting (Pvt) Ltd.

CGD Consulting
Plot# 7-C. 5th Zulfiqar Comm St.
Phase VIII D H A
Karachi.

Project: Infrastructure Development of Education City, Karachi Phase-1 (4800 Acres)–Package-1-A (I).

Subject: Submission of Revised Work Program

Sir,

With reference to your letter # CGDC/ECP/PKG-1(A)-i/RE/53 dated 25-02-2026 and our recent discussion, we hereby submit the Revised Work Program incorporating all revisions and updates as approved via letter # CGDC/ECP/PKG-1(A)-i/JN/2025/0225/171 dated 25-02-2026 for your review, record and approval.

Kindly note that this Revised Work Program is prepared based on the following assumptions and conditions:

- No further changes in design, drawings, plan & profile, cross-sections or construction methodology.
- No increase, reduction or alteration in the scope of work.
- Full land availability and access to all working areas for execution of the works
- Timely availability of all materials as per the BOQ specifications, including specified material sizes and from approved vendor list.

It is further clarified that any future circumstances including, but not limited to:

- Design / drawing revisions,
- Changes in plan & profile, cross-sections or construction methodology,
- Increase or modification in scope of work,
- Delayed or restricted site access,

shall necessitate a corresponding review and revision of the submitted Work Program, including adjustment of timelines where applicable.

We request your review and approval of the enclosed Revised Work Program.

Best Regards,

Muhammad Ikram
Project Manager
J.N & Co.

4/3/26

Recieved by CGDC

C.c:

- Project Director, PIU
- Project Coordinator, PIU

EDUCATION CITY PROJECT
DY NO: 2337
RECEIVED ON: 6/3/26

Info@jn.com.pk
A-22 KDA Scheme # 1,
Karachi, Pakistan
021 3 4920991
021 3 4920992

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
Infrastructure Development of Education City, Karac		870	20-Jan-25	30-Oct-27
Milestones		870	20-Jan-25	30-Oct-27
A50040	Project Commencement (Notice to proceed)	0	20-Jan-25	
A50050	Project Completion	0		30-Oct-27
Pre Construction Phase		28	20-Jan-25	20-Feb-25
A50010	Mobilization	14	20-Jan-25	04-Feb-25
A50020	Site survey	14	05-Feb-25	20-Feb-25
Construction Phase		841	21-Feb-25	29-Oct-27
Civil & Infrastructure		841	21-Feb-25	29-Oct-27
Road 4		498	21-Feb-25	24-Sep-26
Earthwork		249	21-Feb-25	08-Dec-25
A1002	Cutting and removing trees	14	21-Feb-25	08-Mar-25
A1004	CG	14	01-Mar-25	17-Mar-25
A1005	NGC	14	18-Mar-25	02-Apr-25
A1008	Cut and fill	200	03-Apr-25	21-Nov-25
A1010	Subgrade bottom	14	22-Nov-25	08-Dec-25
Drain works		108	09-Dec-25	13-Apr-26
A1020	Excavation	7	09-Dec-25	16-Dec-25
A1030	Stone Soling	7	17-Dec-25	24-Dec-25
A1040	Lean	2	25-Dec-25	26-Dec-25
A1050	RCC Bed	14	27-Dec-25	12-Jan-26
A1060	RCC Walls	21	13-Jan-26	05-Feb-26
A1100	RCC Slab	49	06-Feb-26	03-Apr-26
A1120	Catch basin	14	28-Mar-26	13-Apr-26
Sewerage works		70	20-Dec-25	11-Mar-26
A1070	Excavation	14	20-Dec-25	05-Jan-26
A1080	Sand cushion	10	06-Jan-26	16-Jan-26
A1085	Sleeves	15	17-Jan-26	03-Feb-26
A1090	RCC pipes	15	17-Jan-26	03-Feb-26
A1105	Manholes	21	04-Feb-26	27-Feb-26
A1110	Backfill	10	28-Feb-26	11-Mar-26
Water supply works		80	20-Mar-26	20-Jun-26

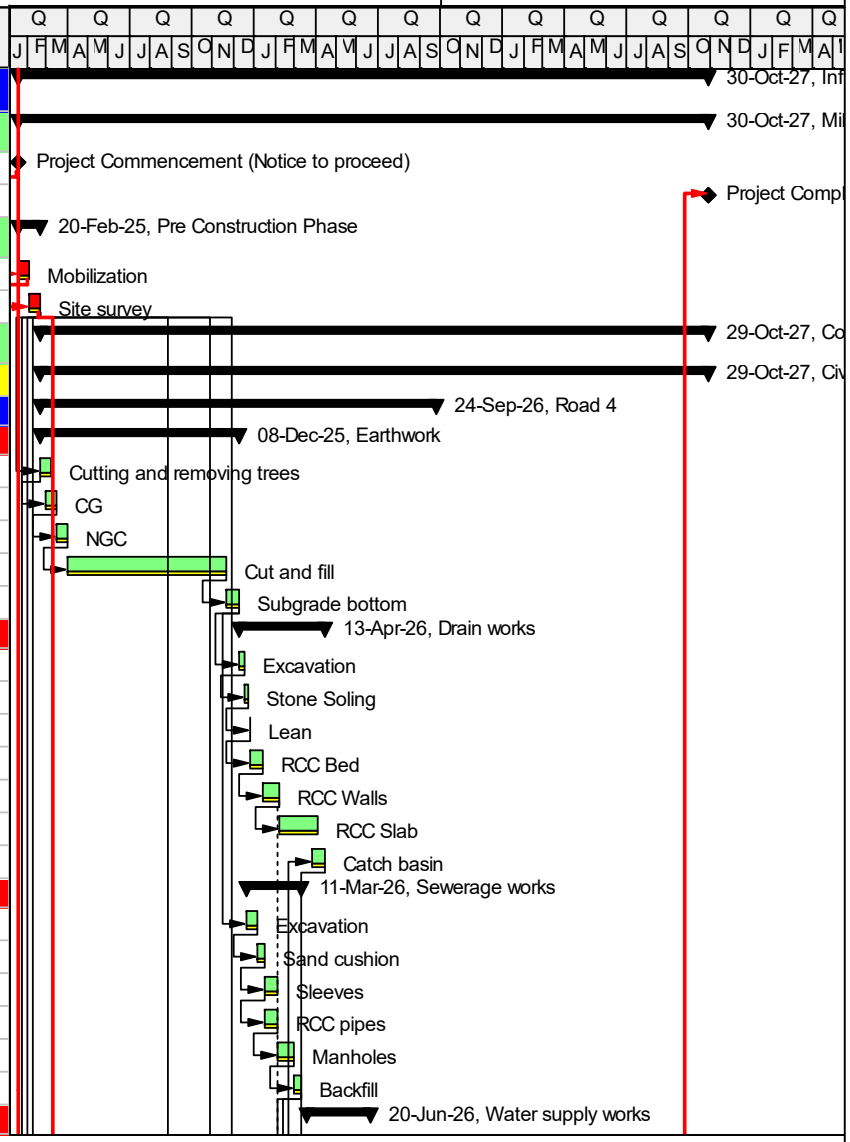

Project Baseline Bar | Remaining Work
Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2870	Excavation	14	20-Mar-26	04-Apr-26
A2880	Sand cushion	10	06-Apr-26	16-Apr-26
A2885	Sleeves	15	17-Apr-26	04-May-26
A2890	PE pipes	15	17-Apr-26	04-May-26
A2895	Inspection chambers	21	05-May-26	28-May-26
A2900	Sand cushion	10	29-May-26	09-Jun-26
A2910	Backfill	10	10-Jun-26	20-Jun-26
Road works		**169**	**12-Mar-26**	**24-Sep-26**
A1121	Subgrade top	14	12-Mar-26	27-Mar-26
A1122	Sub base	28	14-Apr-26	15-May-26
A1130	Aggregate base course	21	16-May-26	09-Jun-26
A1140	Kerbstones	21	16-May-26	09-Jun-26
A1150	Tack coat	21	10-Jun-26	03-Jul-26
A1160	Asphalt concrete binder course	21	26-Jun-26	20-Jul-26
A1170	Prime coat	21	13-Jul-26	05-Aug-26
A1180	Asphalt concrete wearing course	21	29-Jul-26	21-Aug-26
A1190	Pavement marking	15	22-Aug-26	08-Sep-26
A1200	Road Studs	15	22-Aug-26	08-Sep-26
A1210	Signage	14	09-Sep-26	24-Sep-26
Irrigation works		**70**	**30-Jun-26**	**18-Sep-26**
A53130	Excavation + cartage + levelling and compact	7	30-Jun-26	07-Jul-26
A53140	Granular bedding (Sand)	7	08-Jul-26	15-Jul-26
A53145	RCC sleeve pipes	14	16-Jul-26	31-Jul-26
A53150	HDPE pipes (Main Line)	14	16-Jul-26	31-Jul-26
A53160	Chambers	7	01-Aug-26	08-Aug-26
A53162	Sand cushion	7	10-Aug-26	17-Aug-26
A53170	Backfill	7	18-Aug-26	25-Aug-26
A53180	Misc.	7	26-Aug-26	02-Sep-26
A53185	PE pipes (Drip Irrigation)	14	03-Sep-26	18-Sep-26
Road 3		**551**	**01-Mar-25**	**03-Dec-26**
Earthwork		**289**	**01-Mar-25**	**31-Jan-26**
A2005	Cutting and removing trees	14	01-Mar-25	17-Mar-25
A2340	CG	14	10-Mar-25	25-Mar-25

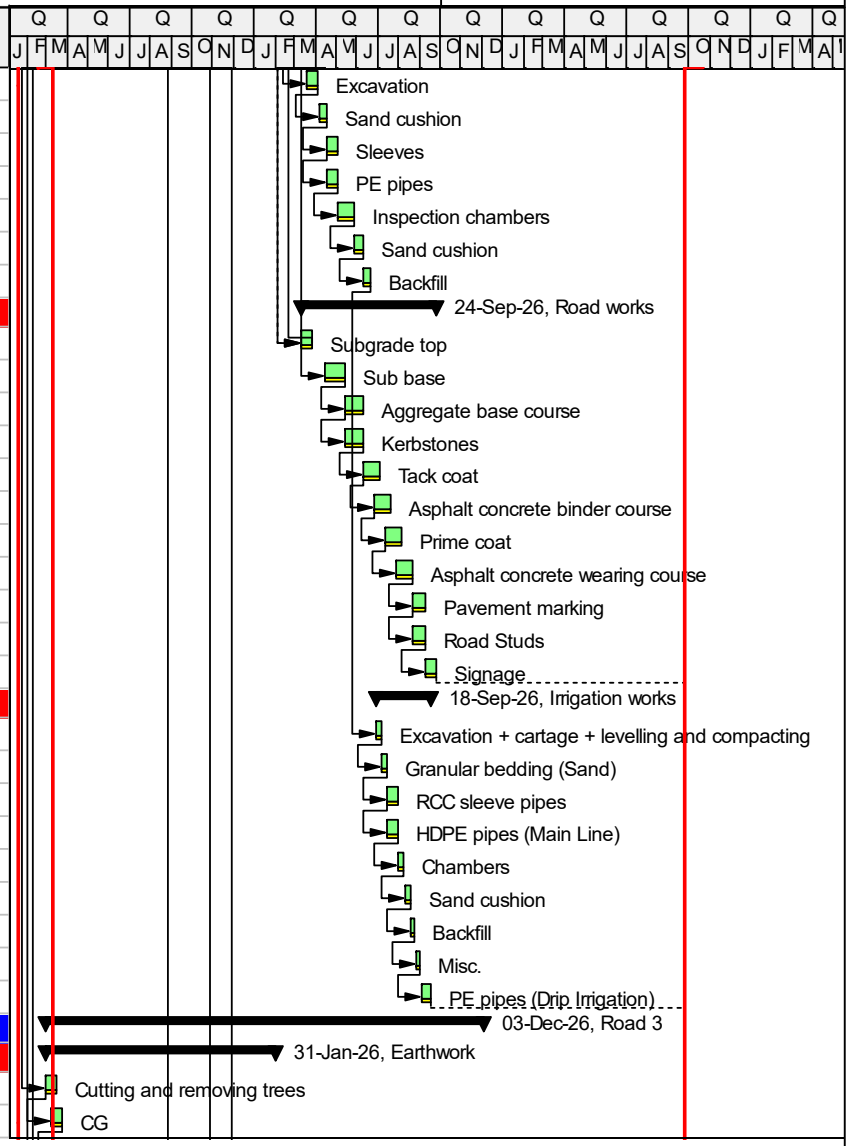

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2350	NGC	14	26-Mar-25	10-Apr-25
A2355	Cut and fill	240	11-Apr-25	15-Jan-26
A2360	Subgrade bottom preparation	14	16-Jan-26	31-Jan-26
Drain works		**108**	**02-Feb-26**	**06-Jun-26**
A51220	Excavation	10	02-Feb-26	12-Feb-26
A51225	Stone Soling	7	13-Feb-26	20-Feb-26
A51230	Lean	4	21-Feb-26	25-Feb-26
A51233	RCC Bed	21	26-Feb-26	21-Mar-26
A51235	RCC Walls	28	23-Mar-26	23-Apr-26
A51245	RCC Slab	28	24-Apr-26	26-May-26
A51255	Catch basin	14	22-May-26	06-Jun-26
Sewerage works		**70**	**13-Feb-26**	**05-May-26**
A2180	Excavation	14	13-Feb-26	28-Feb-26
A2190	Sand cushion	10	02-Mar-26	12-Mar-26
A2195	Sleeves	15	13-Mar-26	30-Mar-26
A2200	RCC pipes	15	13-Mar-26	30-Mar-26
A2202	Manholes	21	31-Mar-26	23-Apr-26
A2204	Backfill	10	24-Apr-26	05-May-26
Water supply works		**80**	**14-May-26**	**14-Aug-26**
A2930	Excavation	14	14-May-26	29-May-26
A2940	Sand cushion	10	30-May-26	10-Jun-26
A2945	Sleeves	15	11-Jun-26	27-Jun-26
A2950	PE pipes	15	11-Jun-26	27-Jun-26
A2955	Inspection Chambers	21	29-Jun-26	22-Jul-26
A2958	Sand cushion	10	23-Jul-26	03-Aug-26
A2962	Backfill	10	04-Aug-26	14-Aug-26
Road works		**182**	**06-May-26**	**03-Dec-26**
A2225	Subgrade top preparation	14	06-May-26	21-May-26
A2230	Sub base	42	08-Jun-26	25-Jul-26
A2240	Aggregate base course	21	27-Jul-26	19-Aug-26
A2242	Kerbstones	21	27-Jul-26	19-Aug-26
A2244	Tack coat	21	20-Aug-26	12-Sep-26
A2246	Asphalt concrete binder course	21	05-Sep-26	29-Sep-26

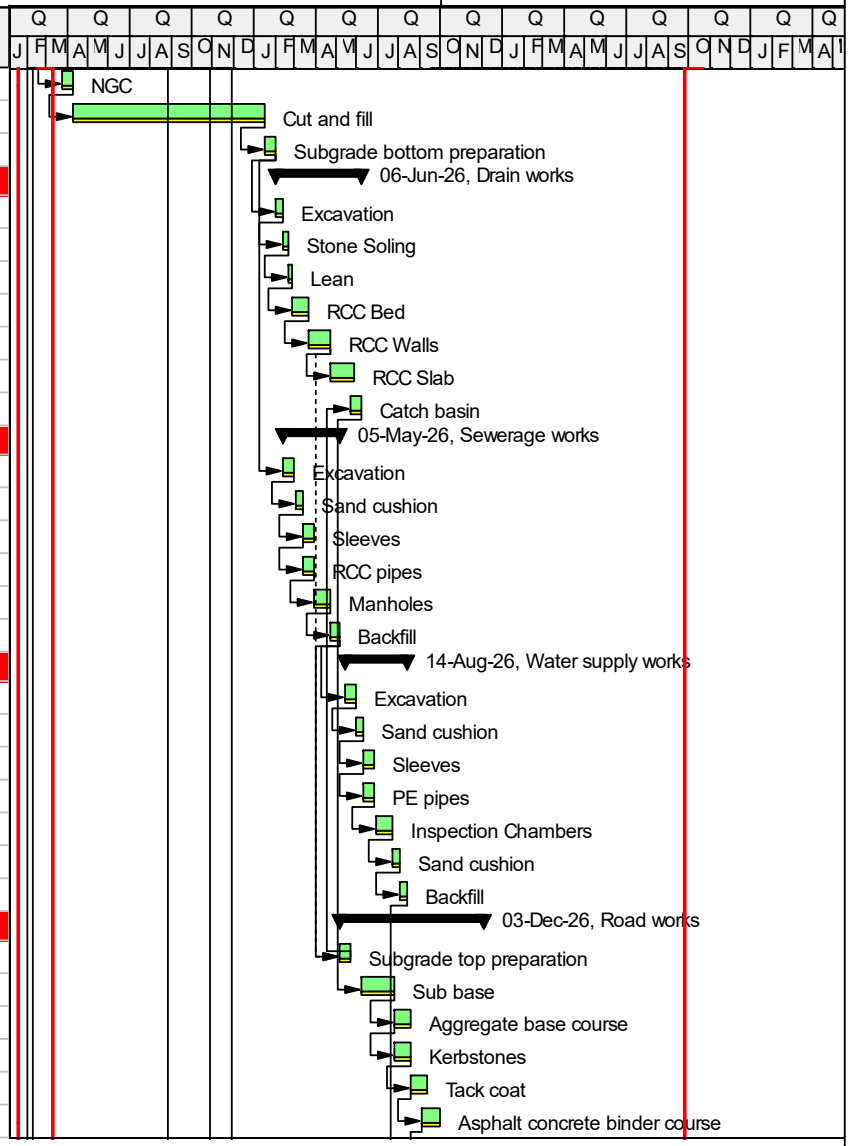

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2248	Prime coat	21	22-Sep-26	15-Oct-26
A2290	Asphalt concrete wearing course	21	08-Oct-26	31-Oct-26
A2300	Pavement marking	14	02-Nov-26	17-Nov-26
A2310	Road Studs	14	02-Nov-26	17-Nov-26
A2320	Signage	14	18-Nov-26	03-Dec-26
Irrigation works		**70**	**24-Aug-26**	**12-Nov-26**
A53310	Excavation + cartage + levelling and compact	7	24-Aug-26	31-Aug-26
A53320	Granular bedding (Sand)	7	01-Sep-26	08-Sep-26
A53325	RCC sleeve pipes	14	09-Sep-26	24-Sep-26
A53330	HDPE pipes (Main Line)	14	09-Sep-26	24-Sep-26
A53340	Chambers	7	25-Sep-26	02-Oct-26
A53345	Sand cushion	7	03-Oct-26	10-Oct-26
A53350	Backfill	7	12-Oct-26	19-Oct-26
A53360	Misc.	7	20-Oct-26	27-Oct-26
A53365	PE pipes (Drip Irrigation)	14	28-Oct-26	12-Nov-26
Road 5		**578**	**10-Mar-25**	**12-Jan-27**
Earthwork		**309**	**10-Mar-25**	**04-Mar-26**
A2365	Cutting and removing trees	14	10-Mar-25	25-Mar-25
A2367	CG	14	18-Mar-25	02-Apr-25
A2369	NGC	14	03-Apr-25	18-Apr-25
A2370	Cut and fill	260	19-Apr-25	16-Feb-26
A2380	Subgrade bottom preparation	14	17-Feb-26	04-Mar-26
Drain works		**112**	**05-Mar-26**	**13-Jul-26**
A2390	Excavation	14	05-Mar-26	20-Mar-26
A2400	Stone Soling	10	21-Mar-26	01-Apr-26
A2410	Lean	4	02-Apr-26	06-Apr-26
A2420	RCC Bed	21	07-Apr-26	30-Apr-26
A2430	RCC Walls	28	01-May-26	02-Jun-26
A2460	RCC Slab	28	03-Jun-26	04-Jul-26
A2470	Catch basin	14	27-Jun-26	13-Jul-26
Sewerage works		**74**	**17-Mar-26**	**10-Jun-26**
A2440	Excavation	14	17-Mar-26	01-Apr-26
A2450	Sand cushion	10	02-Apr-26	13-Apr-26

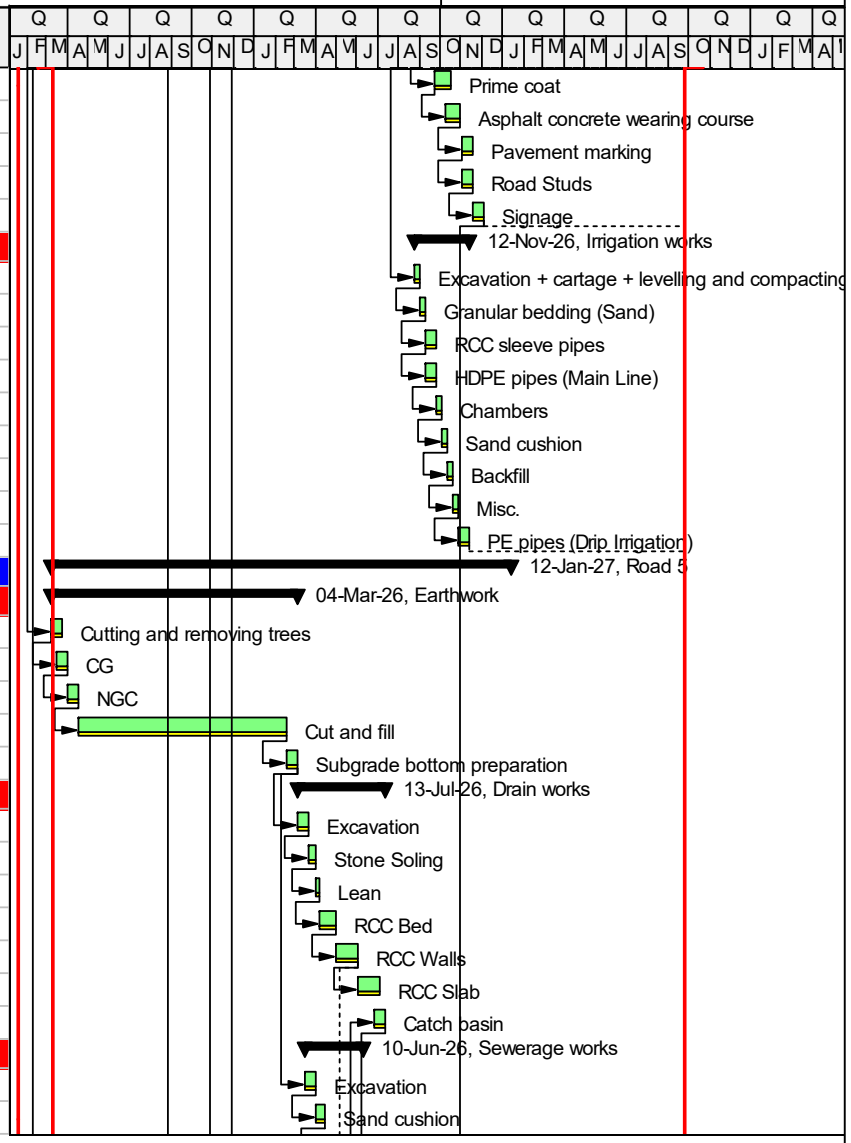

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2451	Sleeves	15	14-Apr-26	30-Apr-26
A2452	RCC pipes	15	14-Apr-26	30-Apr-26
A2454	Manholes	21	01-May-26	25-May-26
A2455	Backfill	14	26-May-26	10-Jun-26
Water supply works		80	19-Jun-26	19-Sep-26
A3002	Excavation	14	19-Jun-26	04-Jul-26
A3004	Sand cushion	10	06-Jul-26	16-Jul-26
A3007	Sleeves	15	17-Jul-26	03-Aug-26
A3010	PE pipes	15	17-Jul-26	03-Aug-26
A3015	Inspection Chambers	21	04-Aug-26	27-Aug-26
A3020	Sand cushion	10	28-Aug-26	08-Sep-26
A3030	Backfill	10	09-Sep-26	19-Sep-26
Road works		185	11-Jun-26	12-Jan-27
A2488	Subgrade top preparation	14	11-Jun-26	26-Jun-26
A2490	Sub base	49	14-Jul-26	08-Sep-26
A2500	Aggregate base course	21	09-Sep-26	02-Oct-26
A2510	Kerbstones	21	09-Sep-26	02-Oct-26
A2512	Tack coat	21	03-Oct-26	27-Oct-26
A2530	Asphalt concrete binder course	21	20-Oct-26	12-Nov-26
A2532	Prime coat	21	05-Nov-26	28-Nov-26
A2550	Asphalt concrete wearing course	21	21-Nov-26	15-Dec-26
A2560	Pavement marking	14	16-Dec-26	31-Dec-26
A2570	Road Studs	14	16-Dec-26	31-Dec-26
A2580	Signage	10	01-Jan-27	12-Jan-27
Irrigation works		70	29-Sep-26	18-Dec-26
A53400	Excavation + cartage + levelling and compact	7	29-Sep-26	06-Oct-26
A53410	Granular bedding (Sand)	7	07-Oct-26	14-Oct-26
A53415	RCC sleeve pipes	14	15-Oct-26	30-Oct-26
A53420	HDPE pipes (Main Line)	14	15-Oct-26	30-Oct-26
A53430	Chambers	7	31-Oct-26	07-Nov-26
A53435	Sand cushion	7	09-Nov-26	16-Nov-26
A53440	Backfill	7	17-Nov-26	24-Nov-26
A53450	Misc.	7	25-Nov-26	02-Dec-26

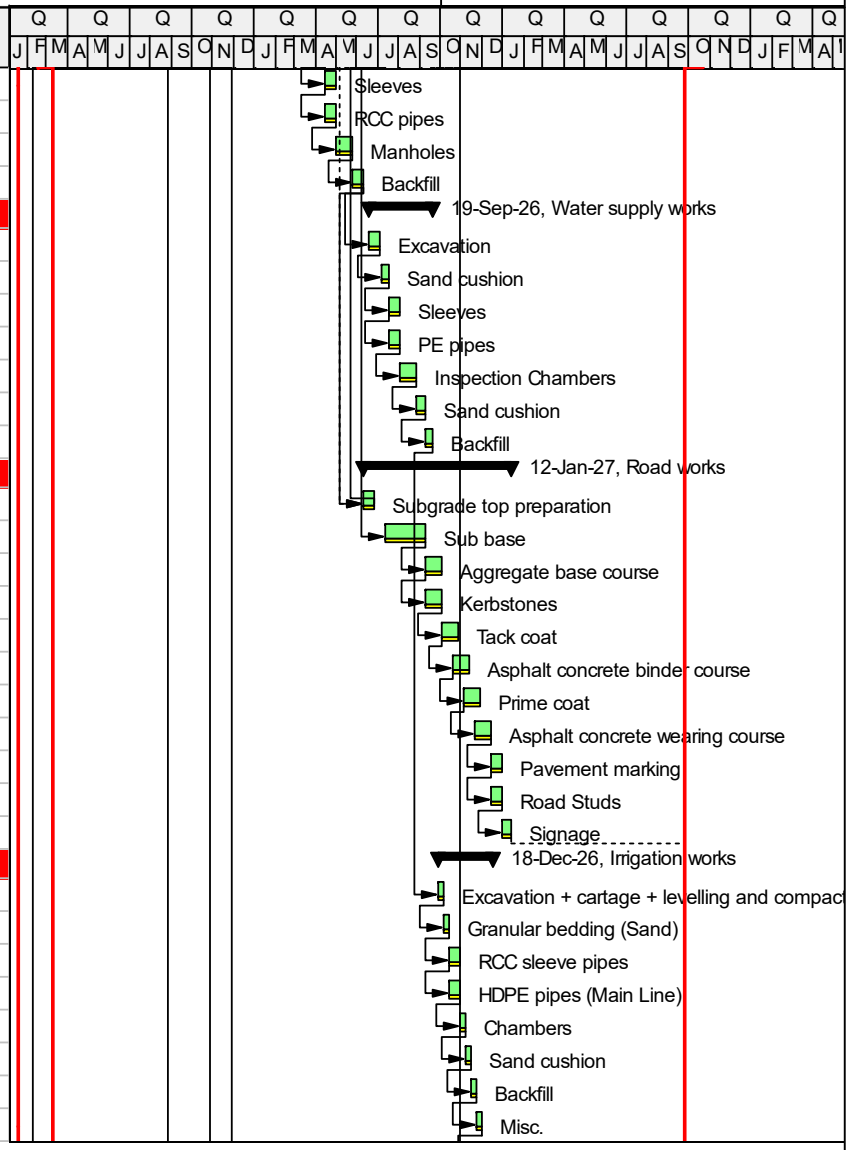

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A53455	PE pipes (Drip Irrigation)	14	03-Dec-26	18-Dec-26
Road 2		577	18-Mar-25	19-Jan-27
Earthwork		319	18-Mar-25	24-Mar-26
A2595	Cutting and removing trees	14	18-Mar-25	02-Apr-25
A2597	CG	14	26-Mar-25	10-Apr-25
A2599	NGC	14	11-Apr-25	26-Apr-25
A51300	Cut and fill	270	28-Apr-25	07-Mar-26
A51310	Subgrade bottom preparation	14	09-Mar-26	24-Mar-26
Drain works		112	25-Mar-26	01-Aug-26
A51320	Excavation	14	25-Mar-26	09-Apr-26
A51330	Stone Soling	10	10-Apr-26	21-Apr-26
A51335	Lean	4	22-Apr-26	25-Apr-26
A51339	RCC Bed	28	27-Apr-26	28-May-26
A51341	RCC Walls	28	29-May-26	30-Jun-26
A51351	RCC Slab	28	01-Jul-26	01-Aug-26
A51361	Catch basin	14	17-Jul-26	01-Aug-26
Sewerage works		70	06-Apr-26	25-Jun-26
A2670	Excavation	14	06-Apr-26	21-Apr-26
A2680	Sand cushion	10	22-Apr-26	02-May-26
A2682	Sleeves	15	04-May-26	20-May-26
A2683	RCC pipes	15	04-May-26	20-May-26
A2684	Manholes	21	21-May-26	13-Jun-26
A2685	Backfill	10	15-Jun-26	25-Jun-26
Water supply works		83	04-Jul-26	08-Oct-26
A3051	Excavation	14	04-Jul-26	20-Jul-26
A3060	Sand cushion	14	21-Jul-26	05-Aug-26
A3065	Sleeves	10	06-Aug-26	17-Aug-26
A3070	PE pipes	10	06-Aug-26	17-Aug-26
A3075	Inspection chamber	21	18-Aug-26	10-Sep-26
A3080	Sand cushion	14	11-Sep-26	26-Sep-26
A3090	Backfill	10	28-Sep-26	08-Oct-26
Road works		174	01-Jul-26	19-Jan-27
A2718	Subgrade top preparation	14	01-Jul-26	16-Jul-26

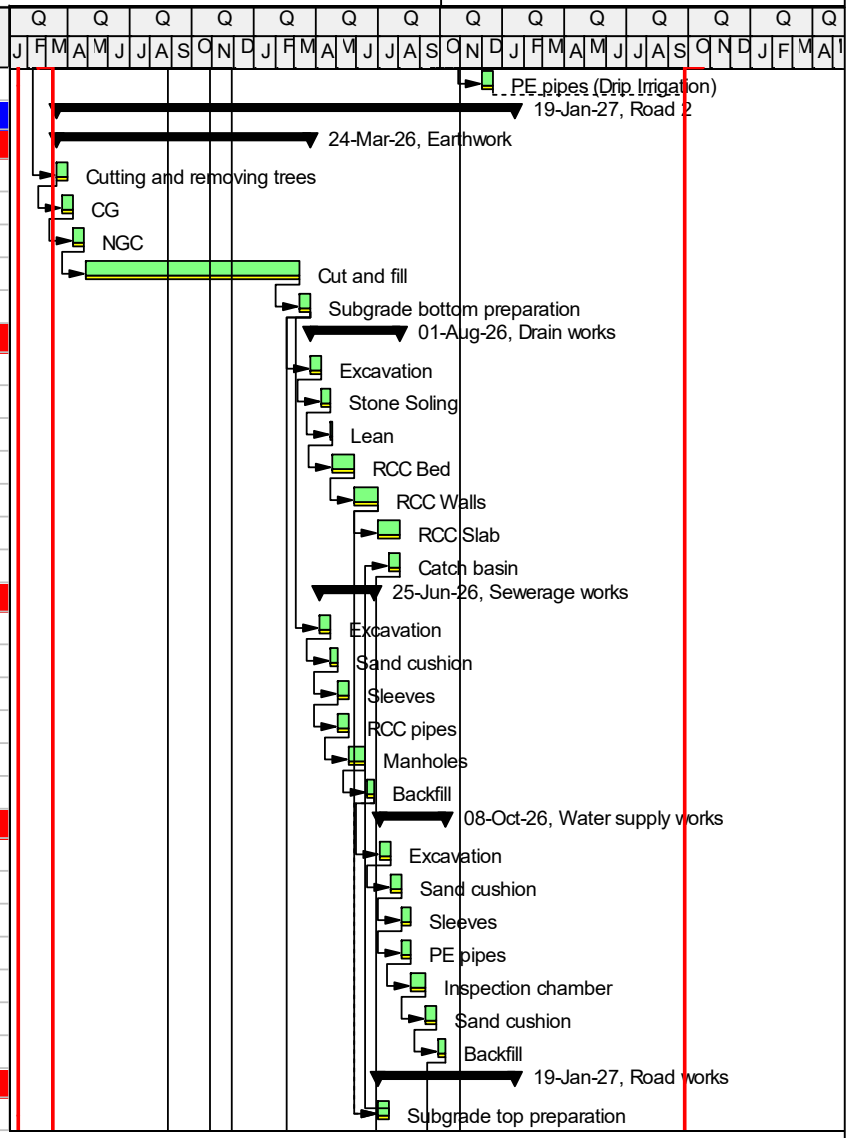

Project Baseline Bar | Remaining Work
Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2720	Sub base	49	03-Aug-26	28-Sep-26
A2730	Aggregate base course	21	29-Sep-26	22-Oct-26
A2740	Kerbstones	21	29-Sep-26	22-Oct-26
A2750	Tack coat	21	23-Oct-26	16-Nov-26
A2760	Asphalt concrete binder course	21	09-Nov-26	02-Dec-26
A2770	Prime coat	21	25-Nov-26	18-Dec-26
A2780	Asphalt concrete wearing course	21	11-Dec-26	04-Jan-27
A2790	Pavement marking	13	05-Jan-27	19-Jan-27
A2800	Road Studs	13	05-Jan-27	19-Jan-27
A2810	Signage	13	05-Jan-27	19-Jan-27
Irrigation works		**70**	**17-Oct-26**	**06-Jan-27**
A53490	Excavation + cartage + levelling and compact	7	17-Oct-26	24-Oct-26
A53500	Granular bedding (Sand)	7	26-Oct-26	02-Nov-26
A53505	RCC sleeve pipes	14	03-Nov-26	18-Nov-26
A53510	HDPE pipes (Main Line)	14	03-Nov-26	18-Nov-26
A53520	Chambers	7	19-Nov-26	26-Nov-26
A53525	Sand cushion	7	27-Nov-26	04-Dec-26
A53530	Backfill	7	05-Dec-26	12-Dec-26
A53540	Misc.	7	14-Dec-26	21-Dec-26
A53545	PE pipes (Drip Irrigation)	14	22-Dec-26	06-Jan-27
Road 6		**231**	**04-Dec-26**	**30-Aug-27**
Earthwork		**63**	**04-Dec-26**	**15-Feb-27**
A3101	Cutting and removing trees	2	04-Dec-26	05-Dec-26
A3103	CG	7	12-Dec-26	19-Dec-26
A3105	NGC	7	21-Dec-26	28-Dec-26
A3110	Cut and fill	28	29-Dec-26	29-Jan-27
A51420	Subgrade bottom preparation	14	30-Jan-27	15-Feb-27
Drain works		**54**	**16-Feb-27**	**19-Apr-27**
A3139	Excavation	7	16-Feb-27	23-Feb-27
A3140	Stone Soling	7	24-Feb-27	03-Mar-27
A3150	Lean	2	04-Mar-27	05-Mar-27
A3160	RCC Bed	10	06-Mar-27	17-Mar-27
A3170	RCC Walls	10	06-Mar-27	17-Mar-27

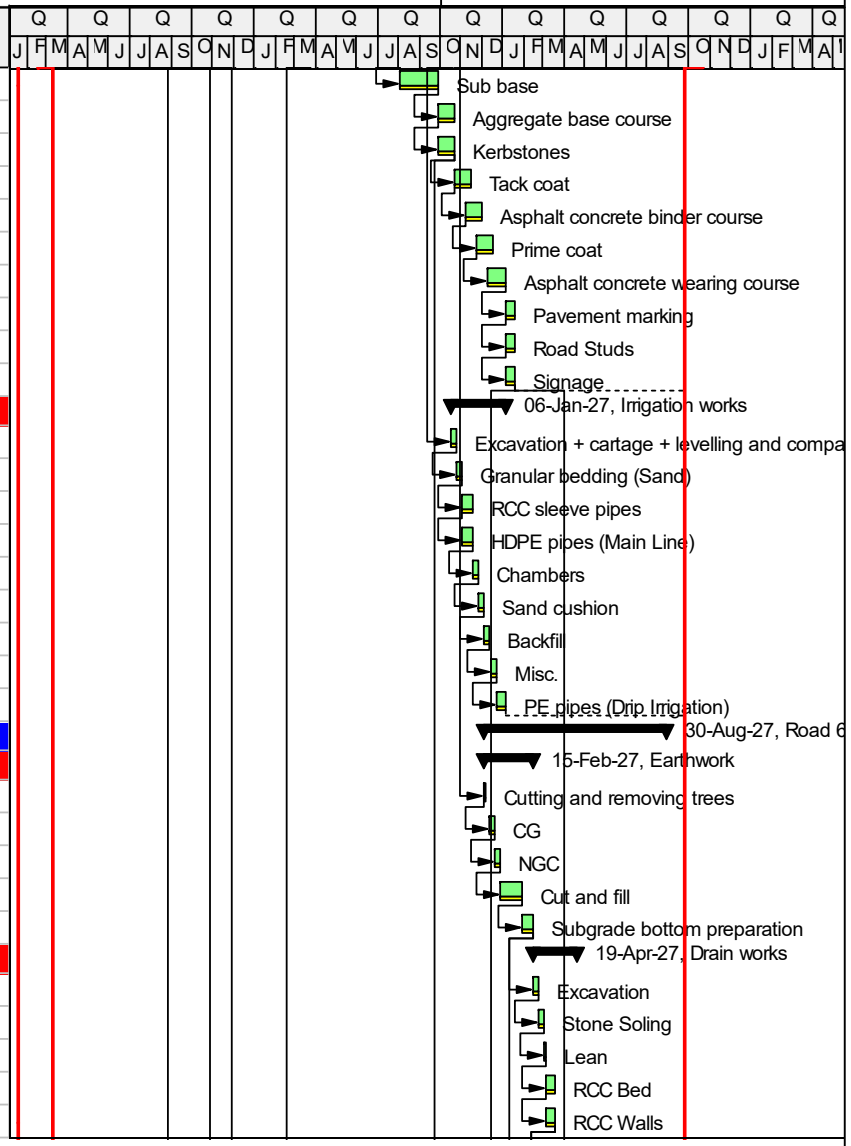

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A3210	RCC Slab	10	18-Mar-27	29-Mar-27
A3320	Catch basin	7	12-Apr-27	19-Apr-27
Sewerage works		70	16-Feb-27	07-May-27
A3189	Excavation	14	16-Feb-27	03-Mar-27
A3190	Sand cushion	14	04-Mar-27	19-Mar-27
A3195	Sleeves	14	20-Mar-27	05-Apr-27
A3200	RCC pipes	14	20-Mar-27	05-Apr-27
A3204	Manholes	14	06-Apr-27	21-Apr-27
A3206	Backfill	14	22-Apr-27	07-May-27
Water supply works		84	08-May-27	13-Aug-27
A3360	Excavation	14	08-May-27	24-May-27
A3370	Sand cushion	14	25-May-27	09-Jun-27
A3375	Sleeves	14	10-Jun-27	25-Jun-27
A3380	PE pipes	14	10-Jun-27	25-Jun-27
A3382	Inspection chamber	14	26-Jun-27	12-Jul-27
A3390	Sand cushion	14	13-Jul-27	28-Jul-27
A3400	Backfill	14	29-Jul-27	13-Aug-27
Road works		61	18-Mar-27	27-May-27
A3238	Subgrade top preparation	21	18-Mar-27	10-Apr-27
A3239	Sub base	21	12-Apr-27	05-May-27
A3241	Aggregate base course	21	13-Apr-27	06-May-27
A3243	Kerbstones	21	13-Apr-27	06-May-27
A3250	Tack coat	21	14-Apr-27	07-May-27
A3260	Asphalt concrete binder course	21	15-Apr-27	08-May-27
A3270	Prime coat	21	16-Apr-27	10-May-27
A3280	Asphalt concrete wearing course	21	17-Apr-27	11-May-27
A3290	Pavement marking	14	12-May-27	27-May-27
A3300	Road Studs	14	12-May-27	27-May-27
A3310	Signage	14	12-May-27	27-May-27
Irrigation works		98	08-May-27	30-Aug-27
A53580	Excavation + cartage + levelling and compact	14	08-May-27	24-May-27
A53590	Granular bedding (Sand)	14	25-May-27	09-Jun-27
A53595	RCC sleeve pipes	14	10-Jun-27	25-Jun-27

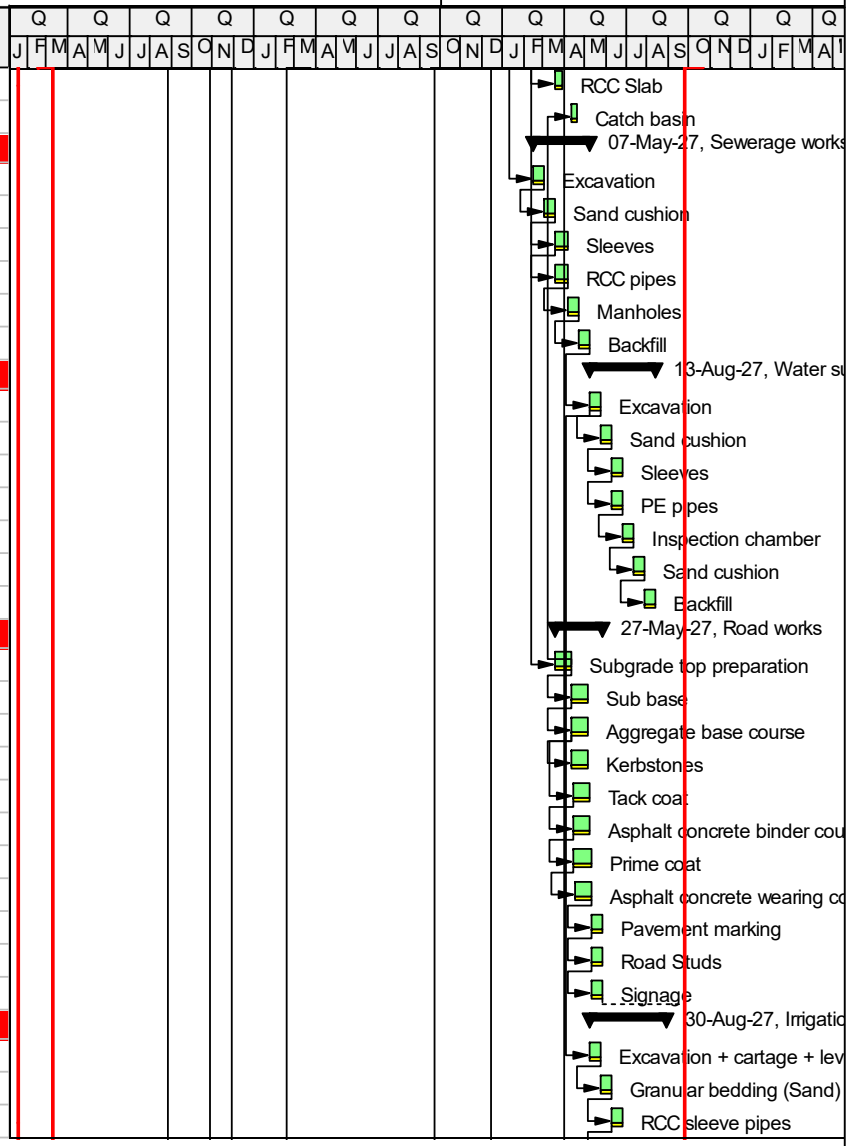

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A53600	HDPE pipes (Main Line)	14	10-Jun-27	25-Jun-27
A53610	Chambers	14	26-Jun-27	12-Jul-27
A53615	Sand cushion	14	13-Jul-27	28-Jul-27
A53620	Backfill	14	29-Jul-27	13-Aug-27
A53630	Misc.	14	29-Jul-27	13-Aug-27
A53640	PE pipes (Drip Irrigation)	14	14-Aug-27	30-Aug-27
Box Culverts		407	02-Oct-25	19-Jan-27
Three Cell		147	02-Oct-25	21-Mar-26
A51480	Excavation	21	02-Oct-25	25-Oct-25
A51490	Dressing and levelling	10	27-Oct-25	06-Nov-25
A51500	Stone soling	21	07-Nov-25	01-Dec-25
A51510	Lean concrete	4	02-Dec-25	05-Dec-25
A51520	RCC foundation	21	06-Dec-25	30-Dec-25
A51530	RCC walls	28	31-Dec-25	31-Jan-26
A51540	RCC top slab	21	02-Feb-26	25-Feb-26
A51550	Formation of embankment	21	26-Feb-26	21-Mar-26
Two Cell		147	02-Oct-25	21-Mar-26
A51570	Excavation	21	02-Oct-25	25-Oct-25
A51580	Dressing and levelling	10	27-Oct-25	06-Nov-25
A51590	Stone soling	21	07-Nov-25	01-Dec-25
A51600	Lean concrete	4	02-Dec-25	05-Dec-25
A51610	RCC foundation	21	06-Dec-25	30-Dec-25
A51620	RCC walls	28	31-Dec-25	31-Jan-26
A51630	RCC top slab	21	02-Feb-26	25-Feb-26
A51640	Formation of embankment	21	26-Feb-26	21-Mar-26
One Cell		72	28-Oct-26	19-Jan-27
A51658	Excavation	7	28-Oct-26	04-Nov-26
A51660	Dressing and levelling	7	05-Nov-26	12-Nov-26
A51670	Stone soling	7	13-Nov-26	20-Nov-26
A51680	Lean concrete	2	21-Nov-26	23-Nov-26
A51690	RCC foundation	14	24-Nov-26	09-Dec-26
A51700	RCC walls	14	10-Dec-26	25-Dec-26
A51710	RCC top slab	14	26-Dec-26	11-Jan-27

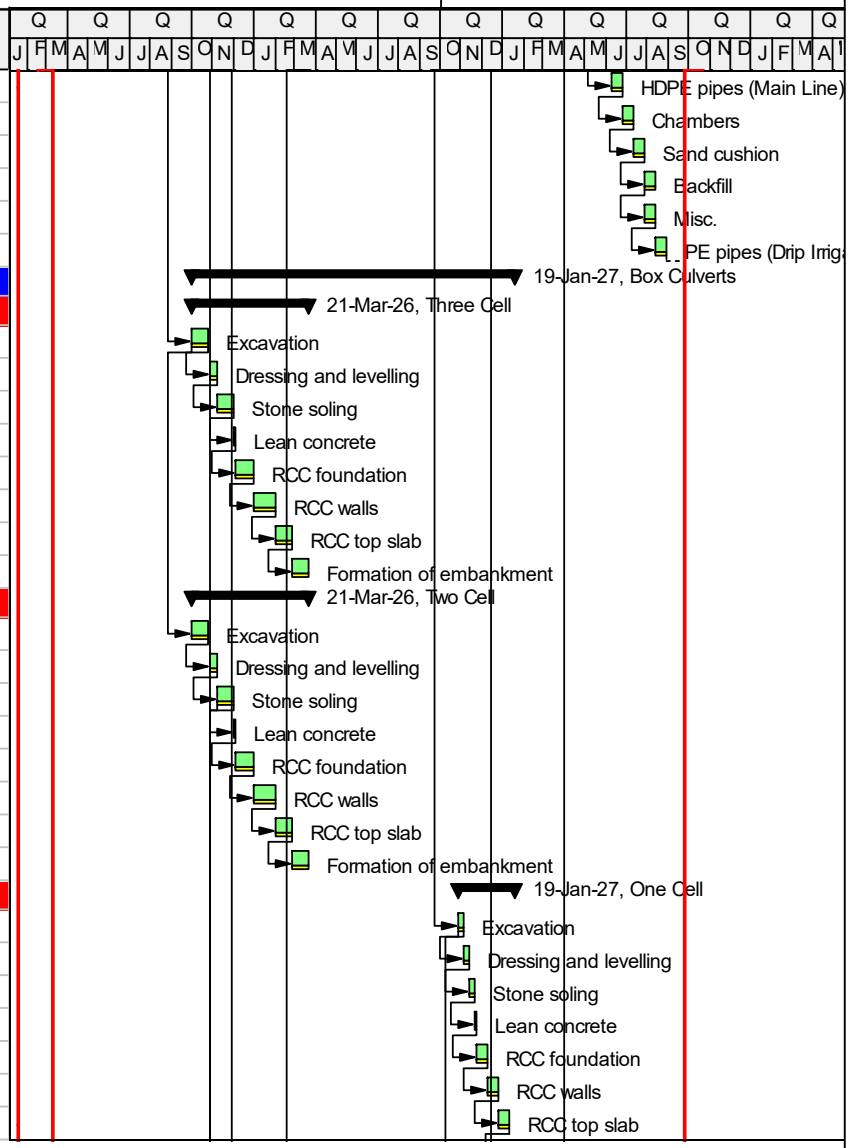

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A51720	Formation of embankment	7	12-Jan-27	19-Jan-27
Horticulture Works		240	20-Jan-27	26-Oct-27
A1490	Garden soil	60	20-Jan-27	30-Mar-27
A1500	Cow dung manure	60	24-Feb-27	04-May-27
A1510	Ground covers	60	31-Mar-27	08-Jun-27
A1520	Live (Dacca) grass	60	05-May-27	13-Jul-27
A1525	Plantation	120	05-May-27	21-Sep-27
A1527	Fountain works	30	22-Sep-27	26-Oct-27
A1530	Matte randum stone in lawn spaces	30	22-Sep-27	26-Oct-27
Water Supply Bore, Reservoir & Pump Station		353	02-Dec-25	16-Jan-27
Tube well		63	02-Dec-25	12-Feb-26
A52330	Boring	21	02-Dec-25	25-Dec-25
A52340	Screen / Blind pipe (uPVC)	14	26-Dec-25	10-Jan-26
A52345	Shrouding graded bajri	7	12-Jan-26	19-Jan-26
A52350	Pump Riser Pipe	7	20-Jan-26	27-Jan-26
A52360	Misc.	14	28-Jan-26	12-Feb-26
Tube well chamber		56	13-Nov-26	16-Jan-27
A50180	Excavation	14	13-Nov-26	28-Nov-26
A50190	RCC foundation	7	30-Nov-26	07-Dec-26
A50200	RCC walls	14	08-Dec-26	23-Dec-26
A50210	Block masonry	7	24-Dec-26	31-Dec-26
A50220	Plaster	7	01-Jan-27	08-Jan-27
A50230	Water proofing	7	01-Jan-27	08-Jan-27
A50240	Roof Slab	7	01-Jan-27	08-Jan-27
A50260	Misc.	7	09-Jan-27	16-Jan-27
Water Reservoir		162	03-Jan-26	10-Jul-26
A50270	Excavation	21	03-Jan-26	27-Jan-26
A50290	Dressing and levelling	14	28-Jan-26	12-Feb-26
A50295	Stone soling	14	13-Feb-26	28-Feb-26
A50300	Lean concrete	4	02-Mar-26	05-Mar-26
A50310	Membrane	7	06-Mar-26	13-Mar-26
A50315	Lean concrete	4	14-Mar-26	18-Mar-26
A50320	RCC foundation	14	19-Mar-26	03-Apr-26

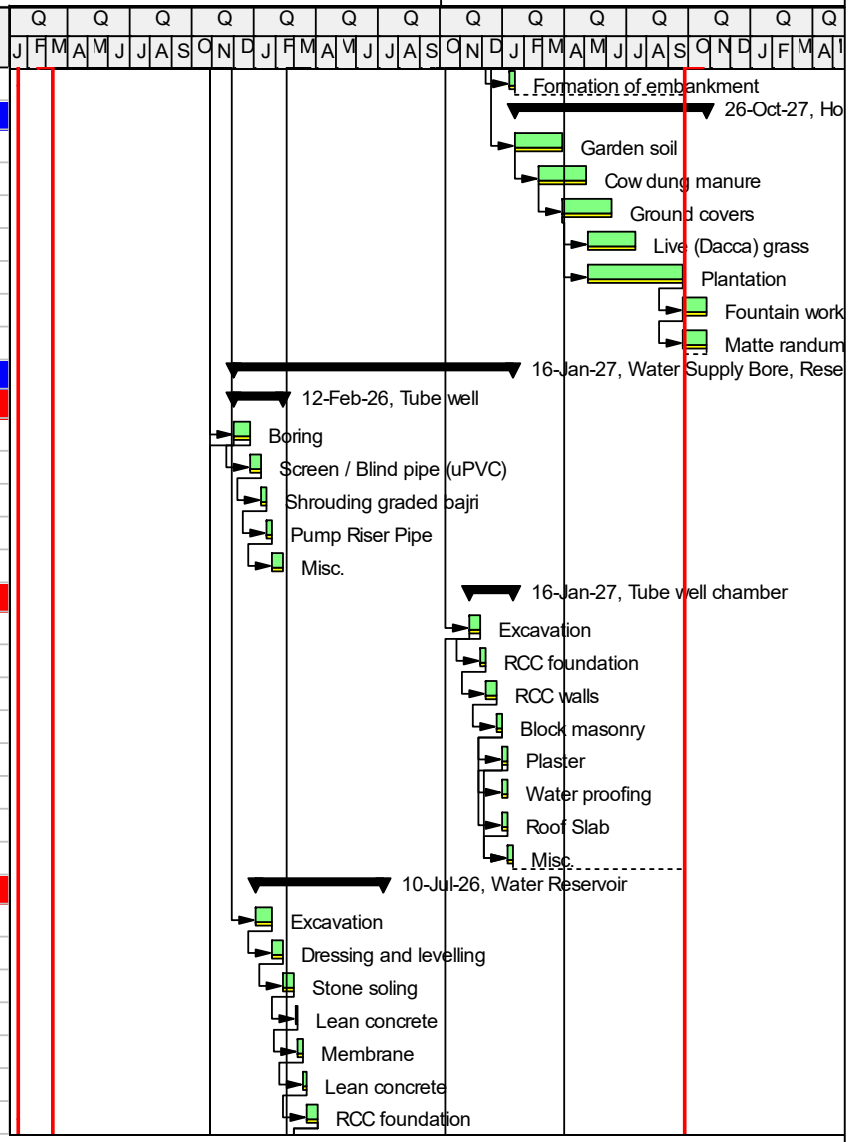

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A50340	RCC walls	21	04-Apr-26	28-Apr-26
A50400	RCC columns	21	04-Apr-26	28-Apr-26
A50410	RCC beams	14	29-Apr-26	14-May-26
A50420	RCC top slab	14	15-May-26	30-May-26
A50425	Internal Plaster	7	15-May-26	22-May-26
A50435	External Membrane	7	01-Jun-26	08-Jun-26
A50437	Block Masonry	7	09-Jun-26	16-Jun-26
A50439	Backfill	14	17-Jun-26	02-Jul-26
A50440	Misc.	7	03-Jul-26	10-Jul-26
Pump Station		84	03-Jul-26	08-Oct-26
A50450	Excavation	14	03-Jul-26	18-Jul-26
A50460	Compaction	7	20-Jul-26	27-Jul-26
A50470	Foundation Slab	14	28-Jul-26	12-Aug-26
A50480	Block masonry	14	13-Aug-26	28-Aug-26
A50490	RCC lintel	7	29-Aug-26	05-Sep-26
A50500	RCC Beam	7	07-Sep-26	14-Sep-26
A50510	RCC Roof Sab	7	15-Sep-26	22-Sep-26
A50520	Parapet wall	7	23-Sep-26	30-Sep-26
A50530	Misc.	7	01-Oct-26	08-Oct-26
Irrigation Bore, Reservoir & Pump Station		353	02-Dec-25	16-Jan-27
Tube well		63	02-Dec-25	12-Feb-26
A50570	Boring	21	02-Dec-25	25-Dec-25
A50590	Screen / Blind pipe (uPVC)	14	26-Dec-25	10-Jan-26
A50595	Shrouding graded bajri	7	12-Jan-26	19-Jan-26
A50600	Pump Riser Pipe	7	20-Jan-26	27-Jan-26
A50620	Misc.	14	28-Jan-26	12-Feb-26
Tube well chamber		56	13-Nov-26	16-Jan-27
A52210	Excavation	14	13-Nov-26	28-Nov-26
A52220	RCC foundation	7	30-Nov-26	07-Dec-26
A52230	RCC walls	14	08-Dec-26	23-Dec-26
A52240	Block masonry	7	24-Dec-26	31-Dec-26
A52250	Plaster	7	01-Jan-27	08-Jan-27
A52260	Water proofing	7	09-Jan-27	16-Jan-27

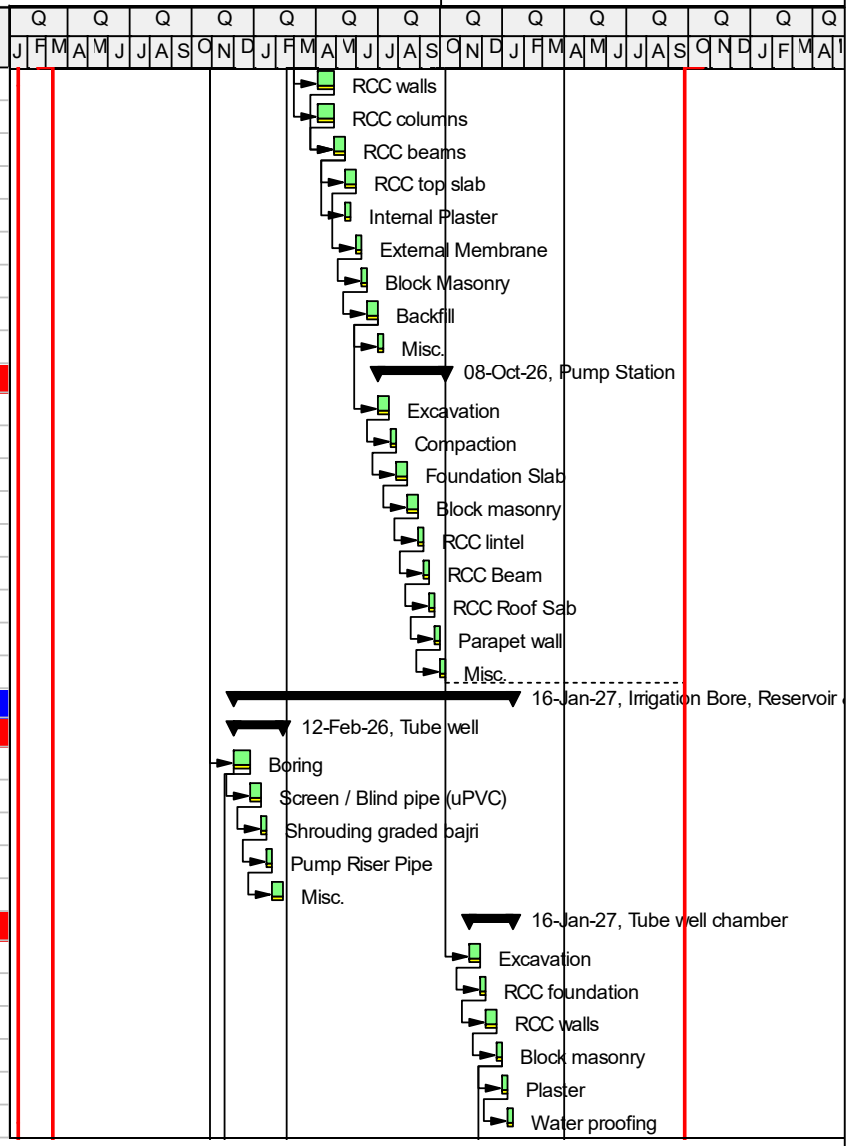

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A52270	Roof slab	7	01-Jan-27	08-Jan-27
A52320	Misc.	7	09-Jan-27	16-Jan-27
Irrigation Reservoir		**161**	**23-Dec-25**	**27-Jun-26**
A50730	Excavation	21	23-Dec-25	15-Jan-26
A50740	Dressing and levelling	10	16-Jan-26	27-Jan-26
A50745	Stone soling	14	28-Jan-26	12-Feb-26
A50750	Lean concrete	4	13-Feb-26	17-Feb-26
A50760	Membrane	10	18-Feb-26	28-Feb-26
A50765	Lean concrete	4	02-Mar-26	05-Mar-26
A50770	RCC foundation	14	06-Mar-26	21-Mar-26
A50790	RCC walls	21	23-Mar-26	15-Apr-26
A50800	RCC columns	21	23-Mar-26	15-Apr-26
A50810	RCC beams	14	16-Apr-26	01-May-26
A50820	RCC top slab	14	02-May-26	18-May-26
A50850	Internal Plaster	7	02-May-26	09-May-26
A50860	External Membrane	7	19-May-26	26-May-26
A50870	Block Masonry	7	27-May-26	03-Jun-26
A50880	Backfill	14	04-Jun-26	19-Jun-26
A50990	Misc.	7	20-Jun-26	27-Jun-26
Pump Station		**77**	**20-Jun-26**	**17-Sep-26**
A50900	Foundation Slab	14	20-Jun-26	06-Jul-26
A50910	Block masonry	7	07-Jul-26	14-Jul-26
A50920	RCC lintel	7	15-Jul-26	22-Jul-26
A50930	RCC Beam	14	23-Jul-26	07-Aug-26
A50940	RCC Roof Sab	14	08-Aug-26	24-Aug-26
A50950	Parapet wall	14	25-Aug-26	09-Sep-26
A50960	Misc.	7	10-Sep-26	17-Sep-26
Bridge		**652**	**15-Apr-25**	**14-May-27**
Civil & Architectural Work		**652**	**15-Apr-25**	**14-May-27**
A3570	Soil test	2	15-Apr-25	16-Apr-25
A3610	Test pile	7	17-Apr-25	24-Apr-25
A3620	Static pile load test on test pile	28	28-May-25	28-Jun-25
A3630	Cast in place piles	30	30-Jun-25	02-Aug-25

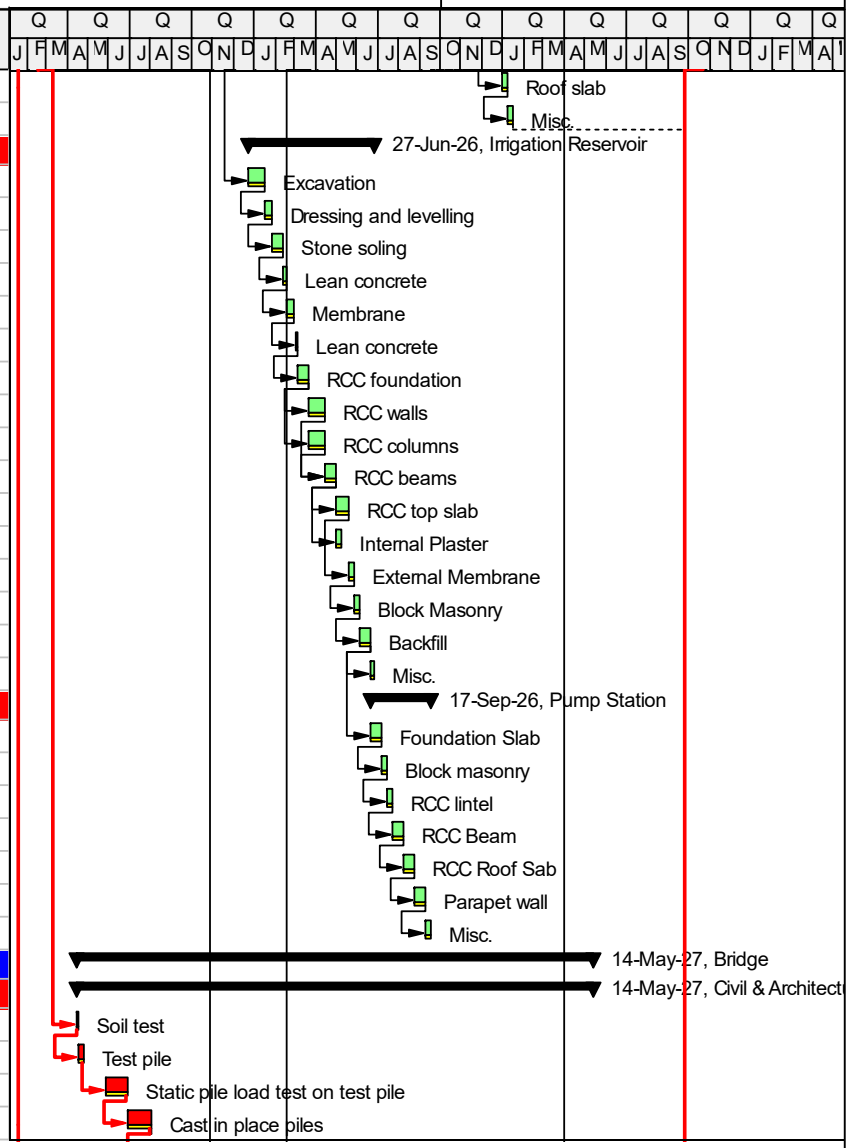

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A3710	Pile integrity testing	21	04-Aug-25	27-Aug-25
A3860	Excavation for pile cap	14	04-Aug-25	19-Aug-25
A3865	Cartage of all excavated material	7	20-Aug-25	27-Aug-25
A3902	Pile cutting and head treatment	14	28-Aug-25	12-Sep-25
A3904	Ground levelling and PCC	14	13-Sep-25	29-Sep-25
A4190	Pile cap	14	30-Sep-25	15-Oct-25
A4200	Pier shafts + Abutment wall	21	18-Nov-25	11-Dec-25
A4205	Retaining wall	56	18-Nov-25	21-Jan-26
A4210	Backfill	14	12-Dec-25	27-Dec-25
A4220	Transom	21	14-Jan-26	06-Feb-26
A4230	Elastomeric bearing pads	7	12-Mar-26	19-Mar-26
A4240	Cast in place Box Girders	275	20-Mar-26	19-Dec-26
A4250	Diaphragm	14	19-Dec-26	05-Jan-27
A4260	Retainer Block + Shear Key	14	05-Jan-27	21-Jan-27
Deck		70	21-Jan-27	13-Apr-27
A51015	Scaffolding	7	21-Jan-27	29-Jan-27
A51025	Formwork installation	14	29-Jan-27	15-Feb-27
A51030	Rebar fixing	14	15-Feb-27	03-Mar-27
A51035	Conduits / pipes / cables for lighting and drain	10	03-Mar-27	15-Mar-27
A51040	Concreting	4	15-Mar-27	19-Mar-27
A51042	Formwork removal and curing	10	19-Mar-27	31-Mar-27
A51045	Expansion joints installation	21	19-Mar-27	13-Apr-27
A51055	Jersey barrier	21	19-Mar-27	13-Apr-27
Approach Road		48	19-Mar-27	14-May-27
A51020	Subgrade preparation	7	19-Mar-27	27-Mar-27
A51070	Sub base	7	27-Mar-27	05-Apr-27
A51110	Aggregate base course	7	05-Apr-27	13-Apr-27
A51120	Tack coat	7	13-Apr-27	21-Apr-27
A51130	Asphalt binder course	7	15-Apr-27	23-Apr-27
A51140	Prime coat	7	17-Apr-27	26-Apr-27
A51150	Asphalt wearing course	7	20-Apr-27	28-Apr-27
A51160	Pavement marking	7	28-Apr-27	06-May-27
A51170	Road studs	7	28-Apr-27	06-May-27

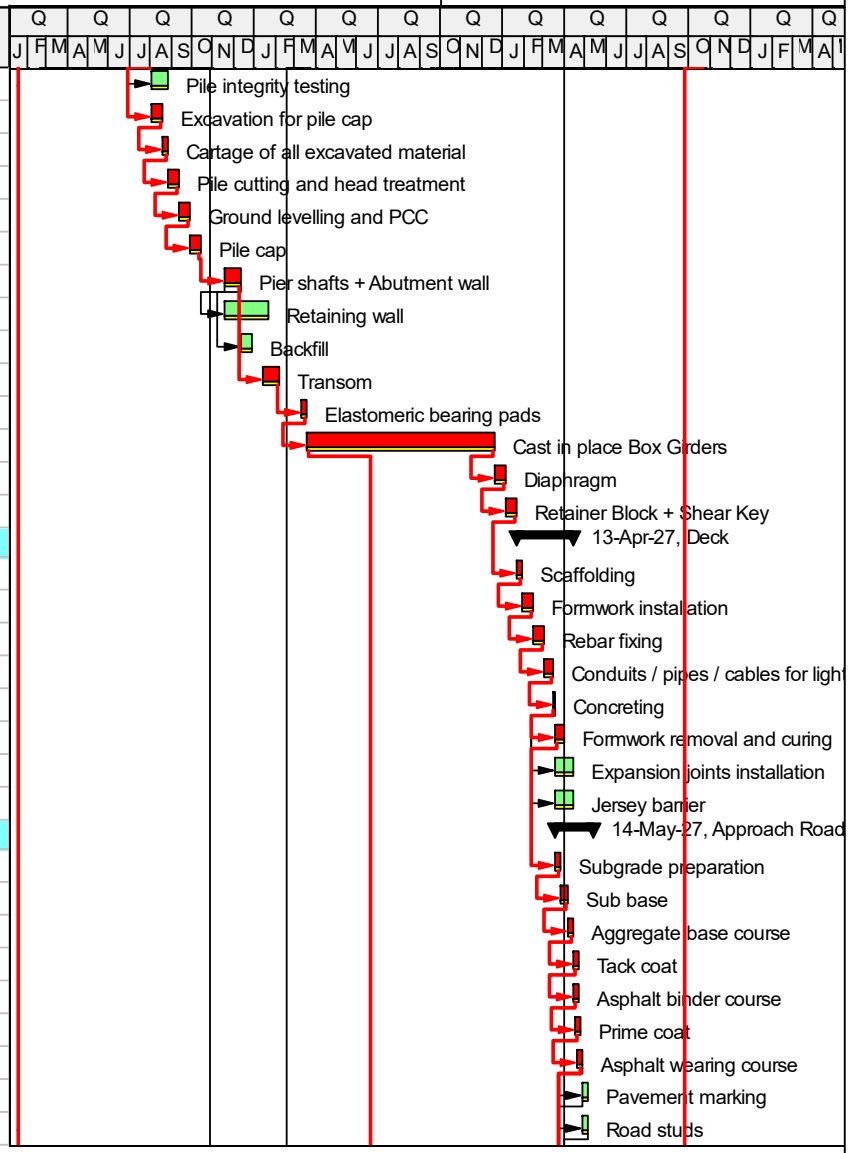

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A51201	Gantry and informatory signs	7	06-May-27	14-May-27
A51205	Railing	7	06-May-27	14-May-27
A51210	Concrete paint	7	06-May-27	14-May-27
Gate House		395	25-Jul-26	29-Oct-27
Civil Works		394	25-Jul-26	28-Oct-27
Arches		387	25-Jul-26	20-Oct-27
Structure		267	25-Jul-26	02-Jun-27
Substructure		147	25-Jul-26	13-Jan-27
A53660	Excavation	28	25-Jul-26	27-Aug-26
A53670	Stone soling	21	27-Aug-26	21-Sep-26
A53680	Lean	21	21-Sep-26	15-Oct-26
A53690	Footings	28	15-Oct-26	17-Nov-26
A53700	Short columns and Shear walls	28	17-Nov-26	19-Dec-26
A53710	Tie Beams	21	19-Dec-26	13-Jan-27
Superstructure		120	13-Jan-27	02-Jun-27
A53720	Construction of Arches	90	13-Jan-27	28-Apr-27
A53730	Launching of Arches	30	28-Apr-27	02-Jun-27
Architecture		120	02-Jun-27	20-Oct-27
A53000	Finishes	120	02-Jun-27	20-Oct-27
Building		157	28-Apr-27	28-Oct-27
Structure		132	28-Apr-27	29-Sep-27
Substructure		90	28-Apr-27	11-Aug-27
A53740	Excavation	10	28-Apr-27	10-May-27
A53750	Stone soling	10	10-May-27	21-May-27
A53760	Lean	7	21-May-27	29-May-27
A53770	Footings	14	29-May-27	15-Jun-27
A53780	Short columns and Shear walls	14	15-Jun-27	01-Jul-27
A53785	Tie beams	14	01-Jul-27	17-Jul-27
A53790	Plinth beams	14	17-Jul-27	03-Aug-27
A53800	Backfill	7	03-Aug-27	11-Aug-27
Superstructure		42	11-Aug-27	29-Sep-27
A53840	Columns	14	11-Aug-27	27-Aug-27
A53850	Walls	14	11-Aug-27	27-Aug-27
A53860	Beams	14	27-Aug-27	13-Sep-27

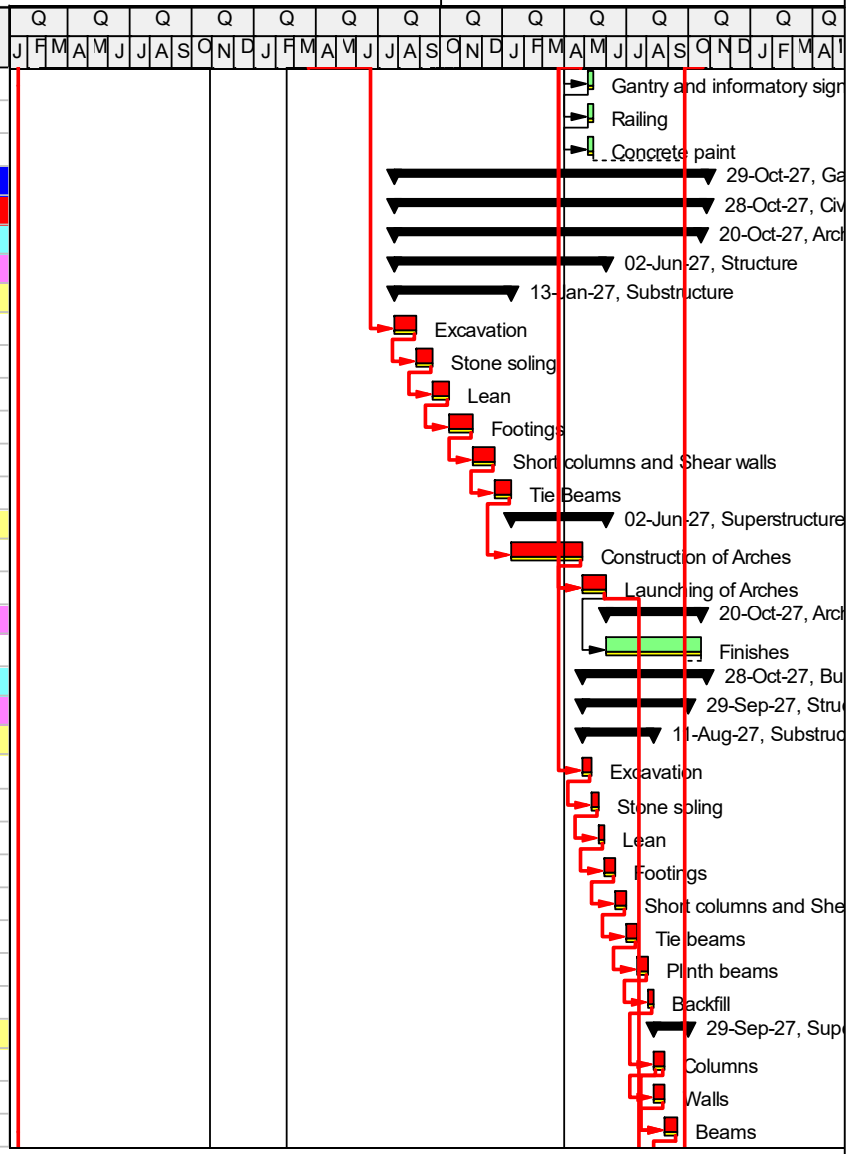

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A53870	Slab	14	13-Sep-27	29-Sep-27
Architecture		25	29-Sep-27	28-Oct-27
A53040	Floor finishes	25	29-Sep-27	28-Oct-27
A53050	Wall finishes	25	29-Sep-27	28-Oct-27
A53060	Ceiling finishes	25	29-Sep-27	28-Oct-27
A53100	Wood / Glass / Metal works	25	29-Sep-27	28-Oct-27
Horticulture Works		26	29-Sep-27	29-Oct-27
A2960	Garden soil	25	29-Sep-27	28-Oct-27
A2970	Cow dung manure	25	30-Sep-27	29-Oct-27
A2980	Live (Dacca) grass	25	30-Sep-27	29-Oct-27
A2981	Trees / Shurbs / Herbs	25	30-Sep-27	29-Oct-27
Plumbing Works		26	29-Sep-27	29-Oct-27
Water Supply Works		25	29-Sep-27	28-Oct-27
A3220	PPR pipes	14	29-Sep-27	15-Oct-27
A3230	Valves	4	15-Oct-27	20-Oct-27
A3240	Electric geysers	7	20-Oct-27	28-Oct-27
Sewerage & Drainage		25	29-Sep-27	28-Oct-27
A3120	Excavation	7	29-Sep-27	07-Oct-27
A3135	uPVC pipes	7	07-Oct-27	15-Oct-27
A3180	Manholes	7	15-Oct-27	23-Oct-27
A3284	Backfill	4	23-Oct-27	28-Oct-27
Plumbing Fixtures		1	28-Oct-27	29-Oct-27
A2990	Providing and fixing European type W.C. pan	1	28-Oct-27	29-Oct-27
A3000	Stainless steel sinks, lavatory basin	1	28-Oct-27	29-Oct-27
A3050	Toilet accessories installation	1	28-Oct-27	29-Oct-27
Electrical Works		25	29-Sep-27	28-Oct-27
A4438	PVC Conduits	7	29-Sep-27	07-Oct-27
A4441	Wiring	10	07-Oct-27	19-Oct-27
A4449	Cables	7	07-Oct-27	15-Oct-27
A4451	Distribution boards	7	19-Oct-27	27-Oct-27
A4680	Light fixtures	7	19-Oct-27	27-Oct-27
A4720	Voice & Data Communication System	7	19-Oct-27	27-Oct-27
A4730	Fire Alarm System	7	19-Oct-27	27-Oct-27
A4735	Earthing System	7	15-Oct-27	23-Oct-27

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A4740	Diesel Generator Set	8	19-Oct-27	28-Oct-27
HVAC		25	29-Sep-27	28-Oct-27
A54150	Piping	15	29-Sep-27	16-Oct-27
A54160	Air Distribution	10	16-Oct-27	28-Oct-27
A54170	VRF Units	10	16-Oct-27	28-Oct-27
Urban Forest		356	01-Dec-25	19-Jan-27
Lake		142	01-Dec-25	14-May-26
A52370	Excavation	21	01-Dec-25	24-Dec-25
A52380	Stone soling	14	25-Dec-25	09-Jan-26
A52390	Lean	7	10-Jan-26	17-Jan-26
A52400	Embankment	21	19-Jan-26	11-Feb-26
A52410	Stone pitching	21	12-Feb-26	07-Mar-26
A52420	Lean	7	09-Mar-26	16-Mar-26
A52430	Membrane	14	17-Mar-26	01-Apr-26
A52440	Lean	7	02-Apr-26	09-Apr-26
A52450	Fibre reinforced concrete	30	10-Apr-26	14-May-26
Island		214	15-May-26	19-Jan-27
A52560	Kerbstones	10	15-May-26	26-May-26
A52570	Crushed stones (Pebbles)	14	27-May-26	11-Jun-26
A52580	Pedestrian Bridges	90	12-Jun-26	24-Sep-26
A52590	Trees	190	12-Jun-26	19-Jan-27
A52600	Misc. (Bush barriers, Precast bench, Sitting bc	190	12-Jun-26	19-Jan-27
Activity Area		214	15-May-26	19-Jan-27
A52465	Compacted Earth	14	15-May-26	30-May-26
A52470	Kerbstones	10	01-Jun-26	11-Jun-26
A52480	Crushed stones (Pebbles)	14	12-Jun-26	27-Jun-26
A52490	Palm Trees	184	19-Jun-26	19-Jan-27
A52500	Misc. (Precast bench, Sitting bollard, Stepping	184	19-Jun-26	19-Jan-27
Bicycle Track		214	15-May-26	19-Jan-27
A52505	Compacted Earth	14	15-May-26	30-May-26
A52510	Kerbstones	10	01-Jun-26	11-Jun-26
A52520	Murrum soil	20	12-Jun-26	04-Jul-26
A52530	Ground cover / Shrubs	170	06-Jul-26	19-Jan-27

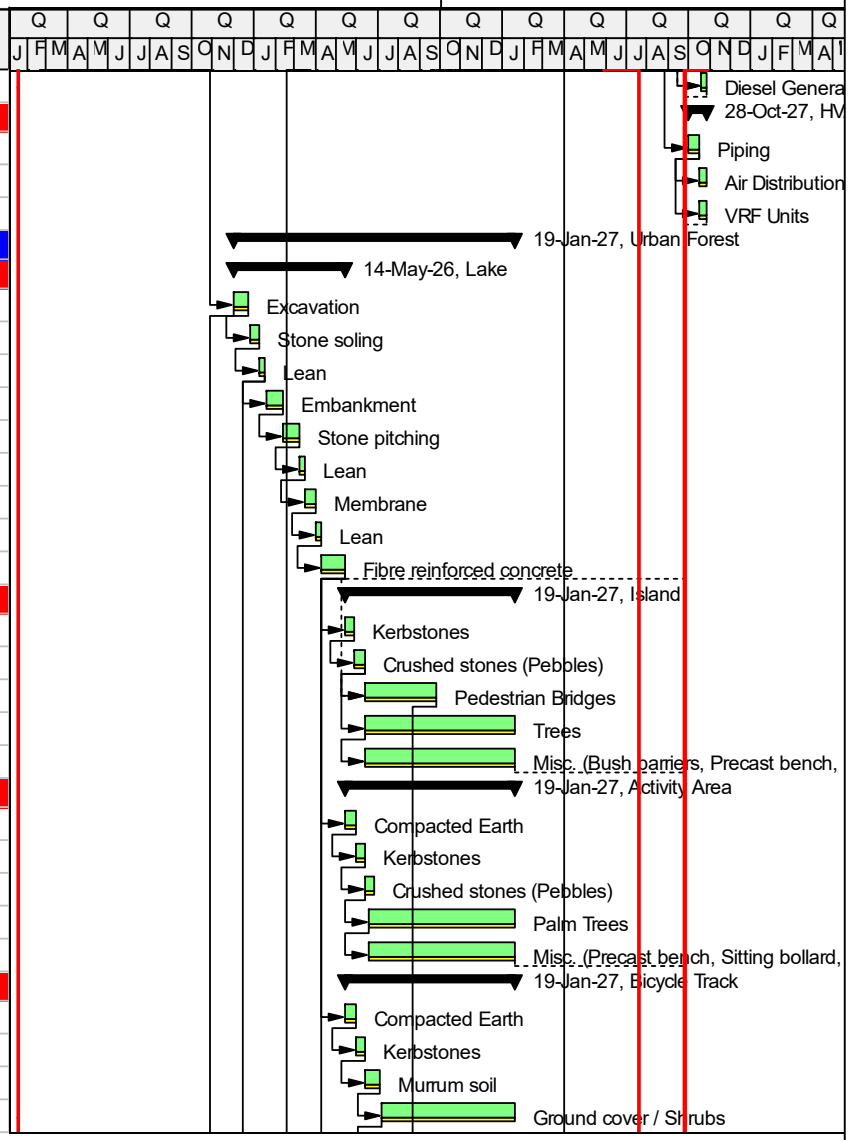

Project Baseline Bar | Remaining Work
Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	FULL SCOPE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A52540	Misc.	170	06-Jul-26	19-Jan-27
Guard Room and Toilet Block		**356**	**01-Dec-25**	**19-Jan-27**
A52620	Substructure	90	01-Dec-25	14-Mar-26
A52630	Superstructure	120	16-Mar-26	01-Aug-26
A52635	OHWT	90	03-Aug-26	14-Nov-26
A52640	Architecture works (wall + floor + ceiling finishe	146	03-Aug-26	19-Jan-27
Miyawaki Forest		**314**	**19-Jan-26**	**19-Jan-27**
A52545	Rough dressing of the area	42	19-Jan-26	07-Mar-26
A52547	Pits	268	09-Mar-26	14-Jan-27
A52549	Supplying and stacking approved garden soil	268	10-Mar-26	15-Jan-27
A52553	Supplying, stacking and spreading cow dung	268	11-Mar-26	16-Jan-27
A52555	Supplying and stacking live (Bermuda) grass i	268	12-Mar-26	18-Jan-27
A52557	Providing and planting Miyawaki Forest area c	268	13-Mar-26	19-Jan-27
Fruit Orchard / Farming Land		**314**	**19-Jan-26**	**19-Jan-27**
A54020	Compacted Earth	42	19-Jan-26	07-Mar-26
A54030	Trees	268	13-Mar-26	19-Jan-27
Entrance		**100**	**25-Sep-26**	**19-Jan-27**
A53975	Compacted Earth	3	25-Sep-26	28-Sep-26
A53980	Crushed stone (Pebbles)	7	29-Sep-26	06-Oct-26
A53990	Stepping Stones	7	29-Sep-26	06-Oct-26
A54010	Trees	90	07-Oct-26	19-Jan-27
BBQ Area		**100**	**25-Sep-26**	**19-Jan-27**
A53940	Compacted Earth	3	25-Sep-26	28-Sep-26
A53945	Kerbstones	7	29-Sep-26	06-Oct-26
A53950	Crushed stones (Pebbles)	7	29-Sep-26	06-Oct-26
A53970	Misc. (Precast bench, Sitting bollard, Boulders	90	07-Oct-26	19-Jan-27
Electrical Works		**20**	**28-Dec-26**	**19-Jan-27**
A4171	uPVC class D pipe	7	28-Dec-26	04-Jan-27
A4172	PVC cables	7	05-Jan-27	12-Jan-27
A4174	DB	6	13-Jan-27	19-Jan-27
A4180	LED Light Pole	6	13-Jan-27	19-Jan-27
A4310	Power Manhole	6	13-Jan-27	19-Jan-27
A4320	Misc. (Isolators, Pull box)	6	13-Jan-27	19-Jan-27
Stream		**214**	**15-May-26**	**19-Jan-27**

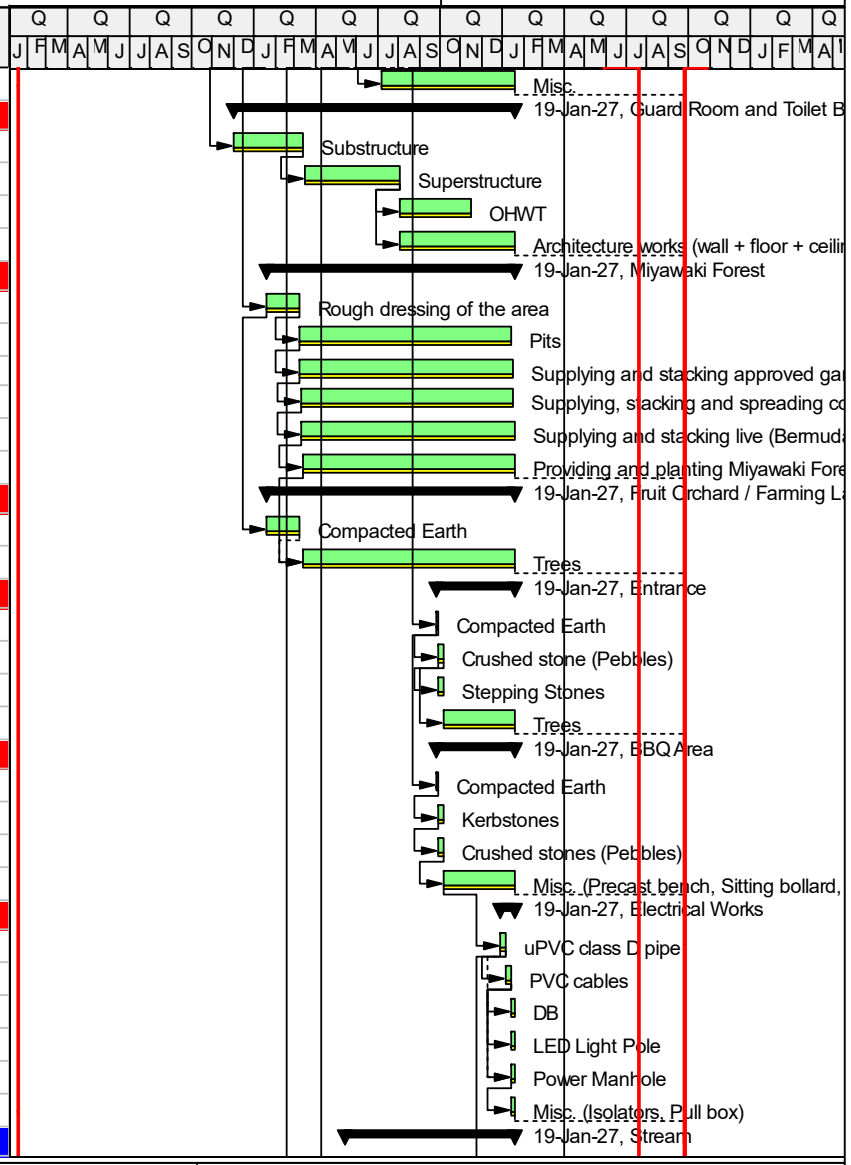

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
Civil Works		148	15-May-26	03-Nov-26
A3640	Excavation	21	15-May-26	08-Jun-26
A3650	Stone soling	14	09-Jun-26	24-Jun-26
A3655	Lean	7	25-Jun-26	02-Jul-26
A3665	Embankment	21	03-Jul-26	27-Jul-26
A3675	Stone pitching	21	28-Jul-26	20-Aug-26
A3685	Lean	10	21-Aug-26	01-Sep-26
A3695	Membrane	14	02-Sep-26	17-Sep-26
A3705	Lean	10	18-Sep-26	29-Sep-26
A3715	Fibre reinforced concrete	30	30-Sep-26	03-Nov-26
Electrical Works		20	28-Dec-26	19-Jan-27
A3838	uPVC class D pipe	7	28-Dec-26	04-Jan-27
A3839	PVC cables	7	05-Jan-27	12-Jan-27
A3840	DB	6	13-Jan-27	19-Jan-27
A3846	LED Light Pole	6	13-Jan-27	19-Jan-27
A3890	Power Manhole	6	13-Jan-27	19-Jan-27
A3900	Misc. (Isolators, Pull box)	6	13-Jan-27	19-Jan-27
Electrical		501	25-Mar-26	29-Oct-27
Bridge		56	23-Aug-27	27-Oct-27
A4323	Construction of Pole foundation	14	23-Aug-27	08-Sep-27
A4324	Octagonal Street lighting pole	14	08-Sep-27	24-Sep-27
A4325	uPVC Class-D Pipes run in Jersey barrier & frc	14	24-Sep-27	11-Oct-27
A4326	Main / Sub main PVC insulated with three cor	14	24-Sep-27	11-Oct-27
A4327	Lighting Control Panel (LCP)	14	24-Sep-27	11-Oct-27
A4328	Street light fixtures	14	24-Sep-27	11-Oct-27
A4329	Flood light fixtures for under Bridge lighting	14	24-Sep-27	11-Oct-27
A4330	Terminal Box	14	24-Sep-27	11-Oct-27
A4331	Copper cables from nearest supply to LCP	14	11-Oct-27	27-Oct-27
A4332	Copper cables from LCP to street lights, unde	14	11-Oct-27	27-Oct-27
A4430	Earth pit with Rod type earth electrode	14	23-Aug-27	08-Sep-27
A4440	PVC insulated copper cable from earth pit to l	14	11-Oct-27	27-Oct-27
Street Lightning		498	25-Mar-26	26-Oct-27
A4802	uPVC Class-D Road Crossing Sleeves for LV (	28	25-Mar-26	25-Apr-26

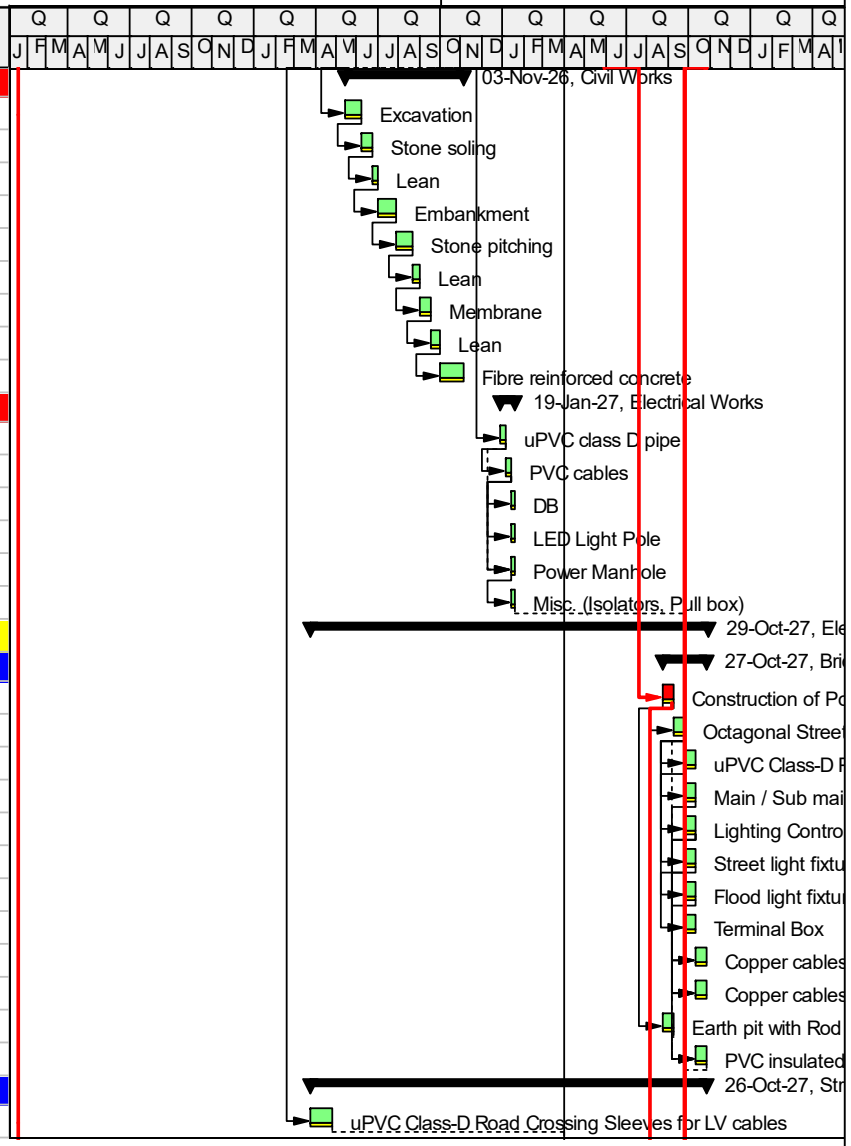

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A4803	Main / Sub main PVC insulated three core co	28	05-May-27	05-Jun-27
A4804	Construction of Pole foundation	30	05-May-27	08-Jun-27
A4806	Octagonal Street lighting pole	60	09-Jun-27	17-Aug-27
A4808	High Hot Dip Galvanized Decorative Urban Po	60	09-Jun-27	17-Aug-27
A4809	Power Manhole	14	07-Jun-27	22-Jun-27
A4810	Earthing	14	09-Jun-27	24-Jun-27
A4812	Terminal Box	14	18-Aug-27	02-Sep-27
A4814	Street light fixture	60	18-Aug-27	26-Oct-27
A4815	LCP	14	18-Aug-27	02-Sep-27
A4816	Strip, underwater light fixtures	60	18-Aug-27	26-Oct-27
A4817	Foundation for Pad Mounted distribution trans	14	23-Jun-27	08-Jul-27
A4818	Pad mounted PMU	14	09-Jul-27	24-Jul-27
A4819	Copper cables from earth pit to LCP/Poles	14	03-Sep-27	18-Sep-27
A4996	Copper cables from PMU to LCP	14	03-Sep-27	18-Sep-27
MV Distribution		44	08-Sep-27	29-Oct-27
A4990	Excavation	10	08-Sep-27	20-Sep-27
A4991	PE pipe	10	20-Sep-27	01-Oct-27
A4994	Aluminium cables	10	20-Sep-27	01-Oct-27
A4995	150 mm (6") dia heavy gauge G.I. pipe	10	20-Sep-27	01-Oct-27
A4997	Straight cable joints	10	20-Sep-27	01-Oct-27
A4998	HT cable markers	10	20-Sep-27	01-Oct-27
A4999	HT heat shrinkable termination kits for cables	10	20-Sep-27	01-Oct-27
A50001	Backfilling of any type of trench already excav	10	01-Oct-27	13-Oct-27
A5060	Foundation for Pad mounted units	10	13-Oct-27	25-Oct-27
A5070	Pad mounted Ring main unit	4	25-Oct-27	29-Oct-27
A5080	Pad Mounted distribution transformers	4	25-Oct-27	29-Oct-27
A5100	Earthing System for Pad Mounted Distribution	4	25-Oct-27	29-Oct-27
Handing Over		1	29-Oct-27	30-Oct-27
A50060	Handing over and taking over	1	29-Oct-27	30-Oct-27

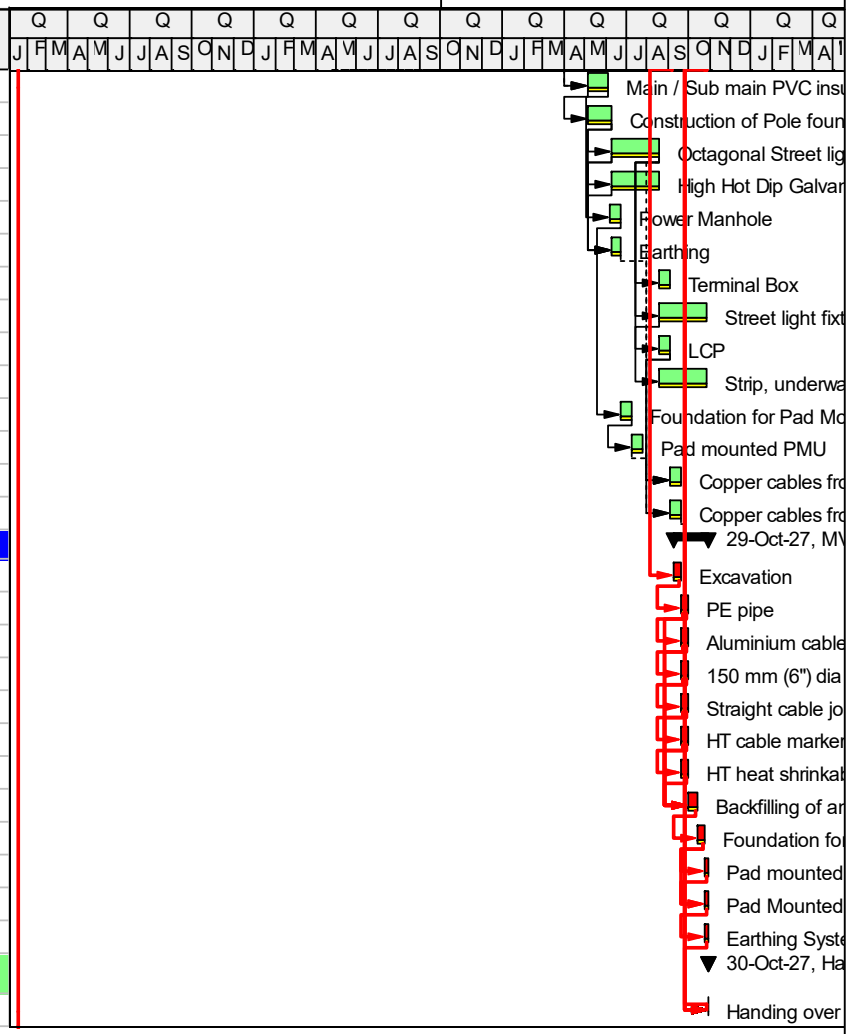

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	EXCLUDING BRIDGE AND GATE HOUSE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
Infrastructure Development of Education City, Karac		626	20-Jan-25	19-Jan-27
Milestones		626	20-Jan-25	19-Jan-27
A50040	Project Commencement (Notice to proceed)	0	20-Jan-25	
A50050	Project Completion	0		19-Jan-27
Pre Construction Phase		28	20-Jan-25	20-Feb-25
A50010	Mobilization	14	20-Jan-25	04-Feb-25
A50020	Site survey	14	05-Feb-25	20-Feb-25
Construction Phase		598	21-Feb-25	19-Jan-27
Civil & Infrastructure		598	21-Feb-25	19-Jan-27
Road 4		498	21-Feb-25	24-Sep-26
Earthwork		249	21-Feb-25	08-Dec-25
A1002	Cutting and removing trees	14	21-Feb-25	08-Mar-25
A1004	CG	14	01-Mar-25	17-Mar-25
A1005	NGC	14	18-Mar-25	02-Apr-25
A1008	Cut and fill	200	03-Apr-25	21-Nov-25
A1010	Subgrade bottom	14	22-Nov-25	08-Dec-25
Drain works		108	09-Dec-25	13-Apr-26
A1020	Excavation	7	09-Dec-25	16-Dec-25
A1030	Stone Soling	7	17-Dec-25	24-Dec-25
A1040	Lean	2	25-Dec-25	26-Dec-25
A1050	RCC Bed	14	27-Dec-25	12-Jan-26
A1060	RCC Walls	21	13-Jan-26	05-Feb-26
A1100	RCC Slab	49	06-Feb-26	03-Apr-26
A1120	Catch basin	14	28-Mar-26	13-Apr-26
Sewerage works		70	20-Dec-25	11-Mar-26
A1070	Excavation	14	20-Dec-25	05-Jan-26
A1080	Sand cushion	10	06-Jan-26	16-Jan-26
A1085	Sleeves	15	17-Jan-26	03-Feb-26
A1090	RCC pipes	15	17-Jan-26	03-Feb-26
A1105	Manholes	21	04-Feb-26	27-Feb-26
A1110	Backfill	10	28-Feb-26	11-Mar-26
Water supply works		80	20-Mar-26	20-Jun-26

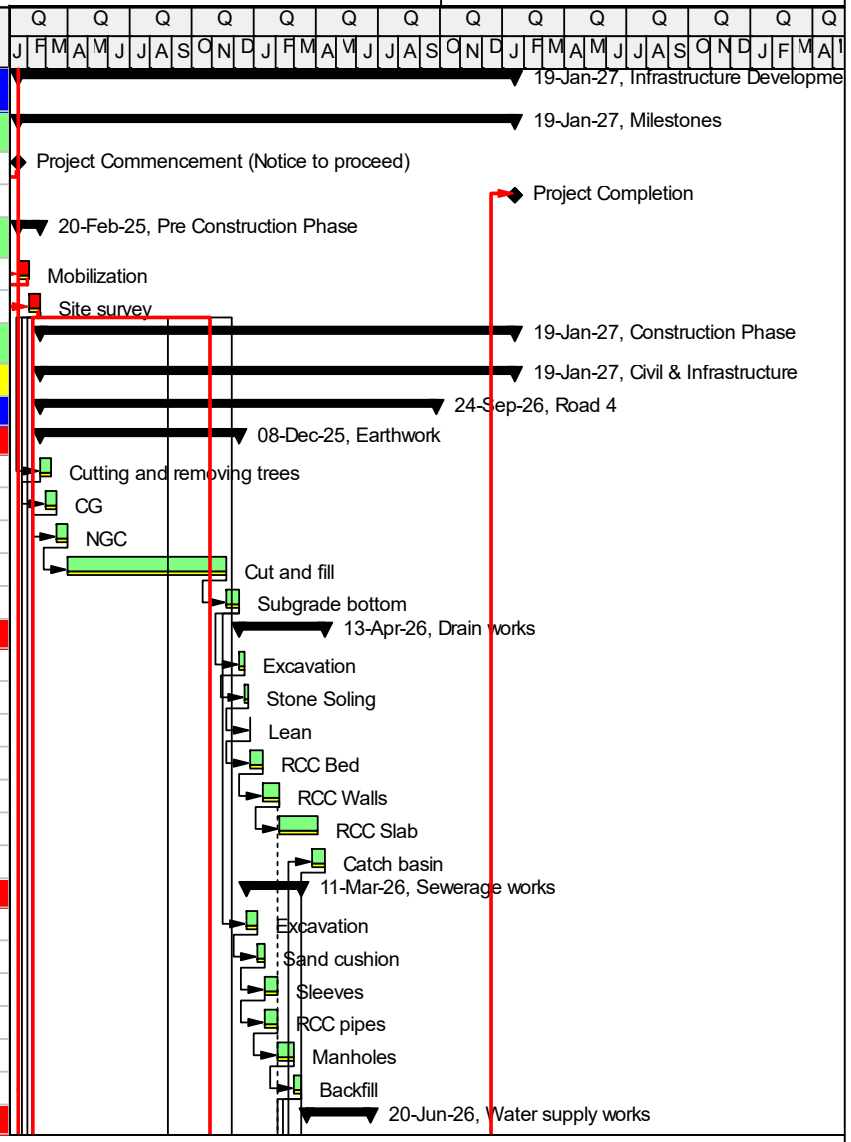

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2870	Excavation	14	20-Mar-26	04-Apr-26
A2880	Sand cushion	10	06-Apr-26	16-Apr-26
A2885	Sleeves	15	17-Apr-26	04-May-26
A2890	PE pipes	15	17-Apr-26	04-May-26
A2895	Inspection chambers	21	05-May-26	28-May-26
A2900	Sand cushion	10	29-May-26	09-Jun-26
A2910	Backfill	10	10-Jun-26	20-Jun-26
Road works		**169**	**12-Mar-26**	**24-Sep-26**
A1121	Subgrade top	14	12-Mar-26	27-Mar-26
A1122	Sub base	28	14-Apr-26	15-May-26
A1130	Aggregate base course	21	16-May-26	09-Jun-26
A1140	Kerbstones	21	16-May-26	09-Jun-26
A1150	Tack coat	21	10-Jun-26	03-Jul-26
A1160	Asphalt concrete binder course	21	26-Jun-26	20-Jul-26
A1170	Prime coat	21	13-Jul-26	05-Aug-26
A1180	Asphalt concrete wearing course	21	29-Jul-26	21-Aug-26
A1190	Pavement marking	15	22-Aug-26	08-Sep-26
A1200	Road Studs	15	22-Aug-26	08-Sep-26
A1210	Signage	14	09-Sep-26	24-Sep-26
Irrigation works		**70**	**30-Jun-26**	**18-Sep-26**
A53130	Excavation + cartage + levelling and compact	7	30-Jun-26	07-Jul-26
A53140	Granular bedding (Sand)	7	08-Jul-26	15-Jul-26
A53145	RCC sleeve pipes	14	16-Jul-26	31-Jul-26
A53150	HDPE pipes (Main Line)	14	16-Jul-26	31-Jul-26
A53160	Chambers	7	01-Aug-26	08-Aug-26
A53162	Sand cushion	7	10-Aug-26	17-Aug-26
A53170	Backfill	7	18-Aug-26	25-Aug-26
A53180	Misc.	7	26-Aug-26	02-Sep-26
A53185	PE pipes (Drip Irrigation)	14	03-Sep-26	18-Sep-26
Road 3		**551**	**01-Mar-25**	**03-Dec-26**
Earthwork		**289**	**01-Mar-25**	**31-Jan-26**
A2005	Cutting and removing trees	14	01-Mar-25	17-Mar-25
A2340	CG	14	10-Mar-25	25-Mar-25

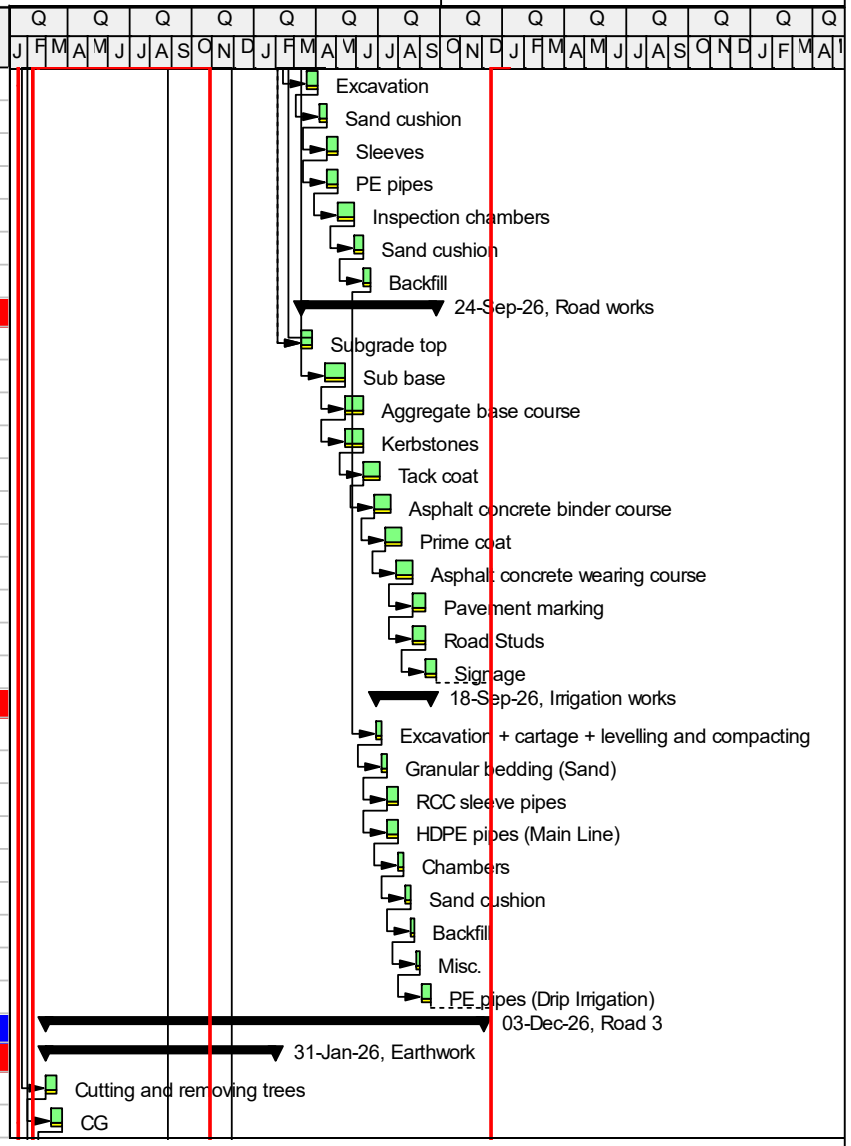

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2350	NGC	14	26-Mar-25	10-Apr-25
A2355	Cut and fill	240	11-Apr-25	15-Jan-26
A2360	Subgrade bottom preparation	14	16-Jan-26	31-Jan-26
Drain works		**108**	**02-Feb-26**	**06-Jun-26**
A51220	Excavation	10	02-Feb-26	12-Feb-26
A51225	Stone Soling	7	13-Feb-26	20-Feb-26
A51230	Lean	4	21-Feb-26	25-Feb-26
A51233	RCC Bed	21	26-Feb-26	21-Mar-26
A51235	RCC Walls	28	23-Mar-26	23-Apr-26
A51245	RCC Slab	28	24-Apr-26	26-May-26
A51255	Catch basin	14	22-May-26	06-Jun-26
Sewerage works		**70**	**13-Feb-26**	**05-May-26**
A2180	Excavation	14	13-Feb-26	28-Feb-26
A2190	Sand cushion	10	02-Mar-26	12-Mar-26
A2195	Sleeves	15	13-Mar-26	30-Mar-26
A2200	RCC pipes	15	13-Mar-26	30-Mar-26
A2202	Manholes	21	31-Mar-26	23-Apr-26
A2204	Backfill	10	24-Apr-26	05-May-26
Water supply works		**80**	**14-May-26**	**14-Aug-26**
A2930	Excavation	14	14-May-26	29-May-26
A2940	Sand cushion	10	30-May-26	10-Jun-26
A2945	Sleeves	15	11-Jun-26	27-Jun-26
A2950	PE pipes	15	11-Jun-26	27-Jun-26
A2955	Inspection Chambers	21	29-Jun-26	22-Jul-26
A2958	Sand cushion	10	23-Jul-26	03-Aug-26
A2962	Backfill	10	04-Aug-26	14-Aug-26
Road works		**182**	**06-May-26**	**03-Dec-26**
A2225	Subgrade top preparation	14	06-May-26	21-May-26
A2230	Sub base	42	08-Jun-26	25-Jul-26
A2240	Aggregate base course	21	27-Jul-26	19-Aug-26
A2242	Kerbstones	21	27-Jul-26	19-Aug-26
A2244	Tack coat	21	20-Aug-26	12-Sep-26
A2246	Asphalt concrete binder course	21	05-Sep-26	29-Sep-26

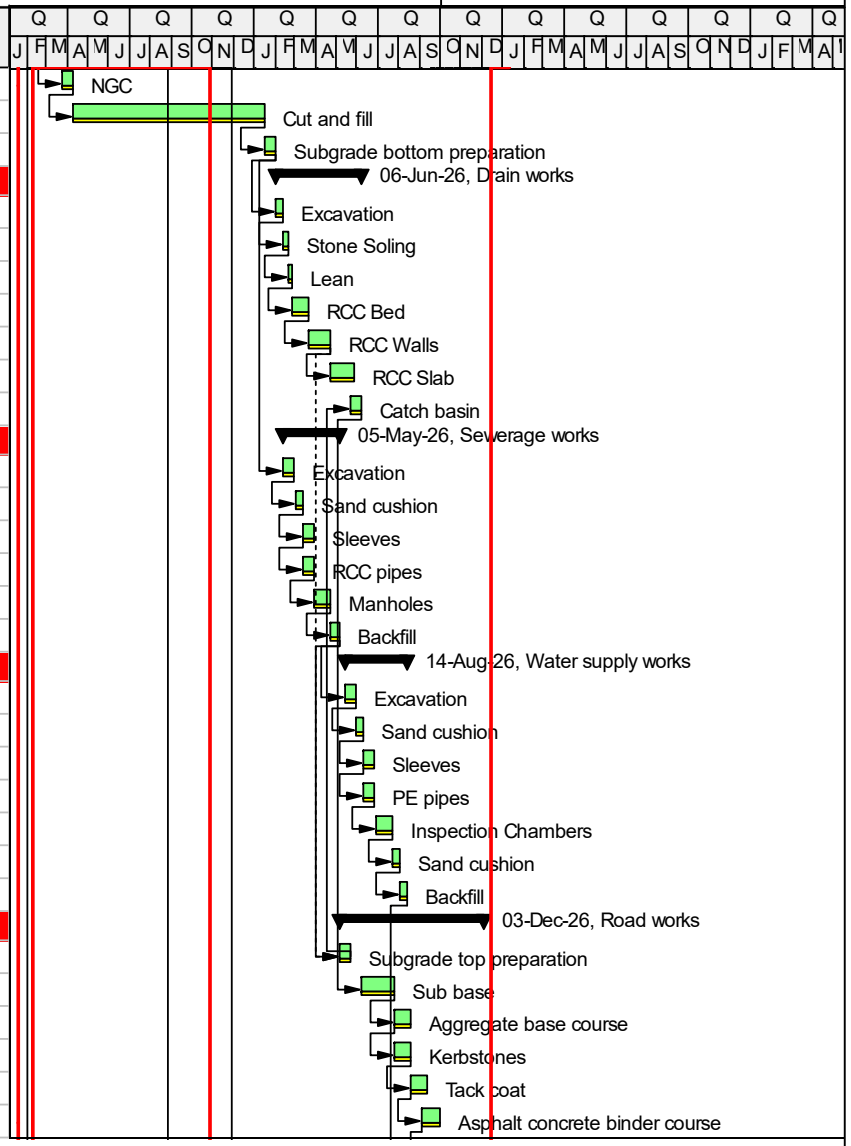

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2248	Prime coat	21	22-Sep-26	15-Oct-26
A2290	Asphalt concrete wearing course	21	08-Oct-26	31-Oct-26
A2300	Pavement marking	14	02-Nov-26	17-Nov-26
A2310	Road Studs	14	02-Nov-26	17-Nov-26
A2320	Signage	14	18-Nov-26	03-Dec-26
Irrigation works		**70**	**24-Aug-26**	**12-Nov-26**
A53310	Excavation + cartage + levelling and compact	7	24-Aug-26	31-Aug-26
A53320	Granular bedding (Sand)	7	01-Sep-26	08-Sep-26
A53325	RCC sleeve pipes	14	09-Sep-26	24-Sep-26
A53330	HDPE pipes (Main Line)	14	09-Sep-26	24-Sep-26
A53340	Chambers	7	25-Sep-26	02-Oct-26
A53345	Sand cushion	7	03-Oct-26	10-Oct-26
A53350	Backfill	7	12-Oct-26	19-Oct-26
A53360	Misc.	7	20-Oct-26	27-Oct-26
A53365	PE pipes (Drip Irrigation)	14	28-Oct-26	12-Nov-26
Road 5		**578**	**10-Mar-25**	**12-Jan-27**
Earthwork		**309**	**10-Mar-25**	**04-Mar-26**
A2365	Cutting and removing trees	14	10-Mar-25	25-Mar-25
A2367	CG	14	18-Mar-25	02-Apr-25
A2369	NGC	14	03-Apr-25	18-Apr-25
A2370	Cut and fill	260	19-Apr-25	16-Feb-26
A2380	Subgrade bottom preparation	14	17-Feb-26	04-Mar-26
Drain works		**112**	**05-Mar-26**	**13-Jul-26**
A2390	Excavation	14	05-Mar-26	20-Mar-26
A2400	Stone Soling	10	21-Mar-26	01-Apr-26
A2410	Lean	4	02-Apr-26	06-Apr-26
A2420	RCC Bed	21	07-Apr-26	30-Apr-26
A2430	RCC Walls	28	01-May-26	02-Jun-26
A2460	RCC Slab	28	03-Jun-26	04-Jul-26
A2470	Catch basin	14	27-Jun-26	13-Jul-26
Sewerage works		**74**	**17-Mar-26**	**10-Jun-26**
A2440	Excavation	14	17-Mar-26	01-Apr-26
A2450	Sand cushion	10	02-Apr-26	13-Apr-26

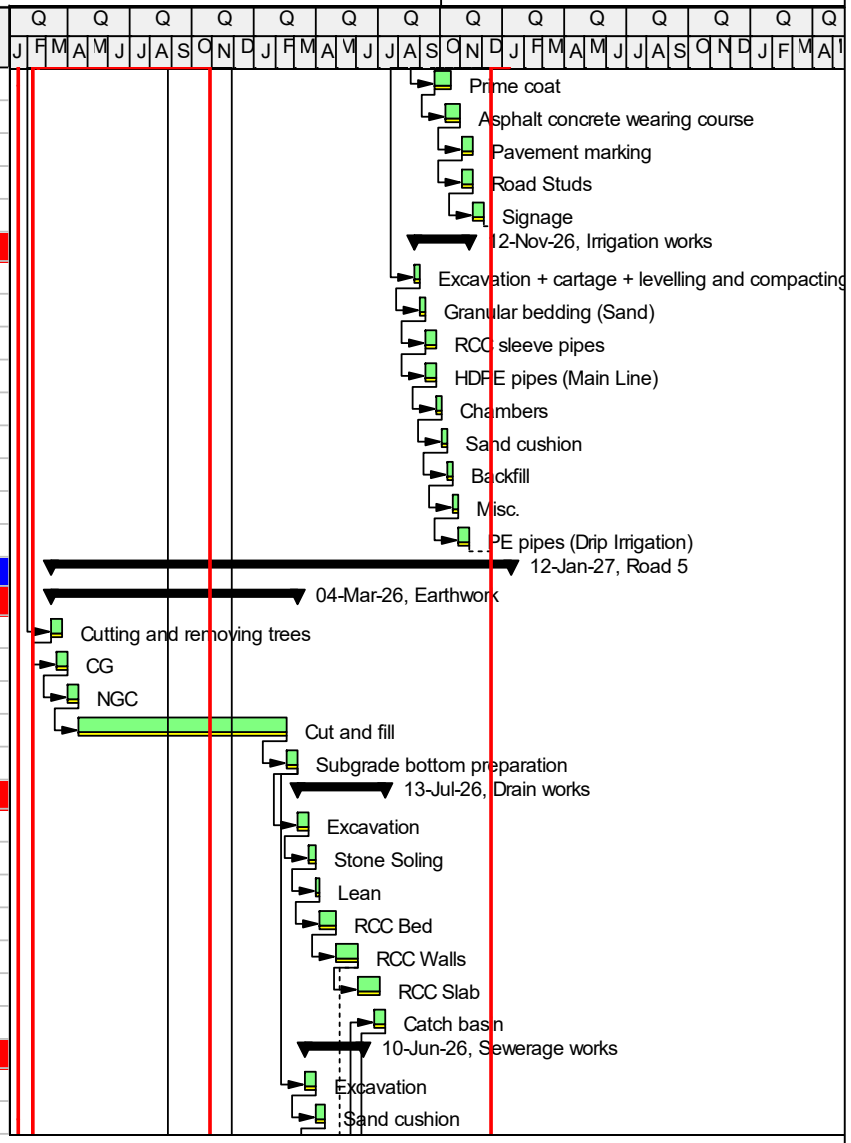

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2451	Sleeves	15	14-Apr-26	30-Apr-26
A2452	RCC pipes	15	14-Apr-26	30-Apr-26
A2454	Manholes	21	01-May-26	25-May-26
A2455	Backfill	14	26-May-26	10-Jun-26
Water supply works		**80**	**19-Jun-26**	**19-Sep-26**
A3002	Excavation	14	19-Jun-26	04-Jul-26
A3004	Sand cushion	10	06-Jul-26	16-Jul-26
A3007	Sleeves	15	17-Jul-26	03-Aug-26
A3010	PE pipes	15	17-Jul-26	03-Aug-26
A3015	Inspection Chambers	21	04-Aug-26	27-Aug-26
A3020	Sand cushion	10	28-Aug-26	08-Sep-26
A3030	Backfill	10	09-Sep-26	19-Sep-26
Road works		**185**	**11-Jun-26**	**12-Jan-27**
A2488	Subgrade top preparation	14	11-Jun-26	26-Jun-26
A2490	Sub base	49	14-Jul-26	08-Sep-26
A2500	Aggregate base course	21	09-Sep-26	02-Oct-26
A2510	Kerbstones	21	09-Sep-26	02-Oct-26
A2512	Tack coat	21	03-Oct-26	27-Oct-26
A2530	Asphalt concrete binder course	21	20-Oct-26	12-Nov-26
A2532	Prime coat	21	05-Nov-26	28-Nov-26
A2550	Asphalt concrete wearing course	21	21-Nov-26	15-Dec-26
A2560	Pavement marking	14	16-Dec-26	31-Dec-26
A2570	Road Studs	14	16-Dec-26	31-Dec-26
A2580	Signage	10	01-Jan-27	12-Jan-27
Irrigation works		**70**	**29-Sep-26**	**18-Dec-26**
A53400	Excavation + cartage + levelling and compact	7	29-Sep-26	06-Oct-26
A53410	Granular bedding (Sand)	7	07-Oct-26	14-Oct-26
A53415	RCC sleeve pipes	14	15-Oct-26	30-Oct-26
A53420	HDPE pipes (Main Line)	14	15-Oct-26	30-Oct-26
A53430	Chambers	7	31-Oct-26	07-Nov-26
A53435	Sand cushion	7	09-Nov-26	16-Nov-26
A53440	Backfill	7	17-Nov-26	24-Nov-26
A53450	Misc.	7	25-Nov-26	02-Dec-26

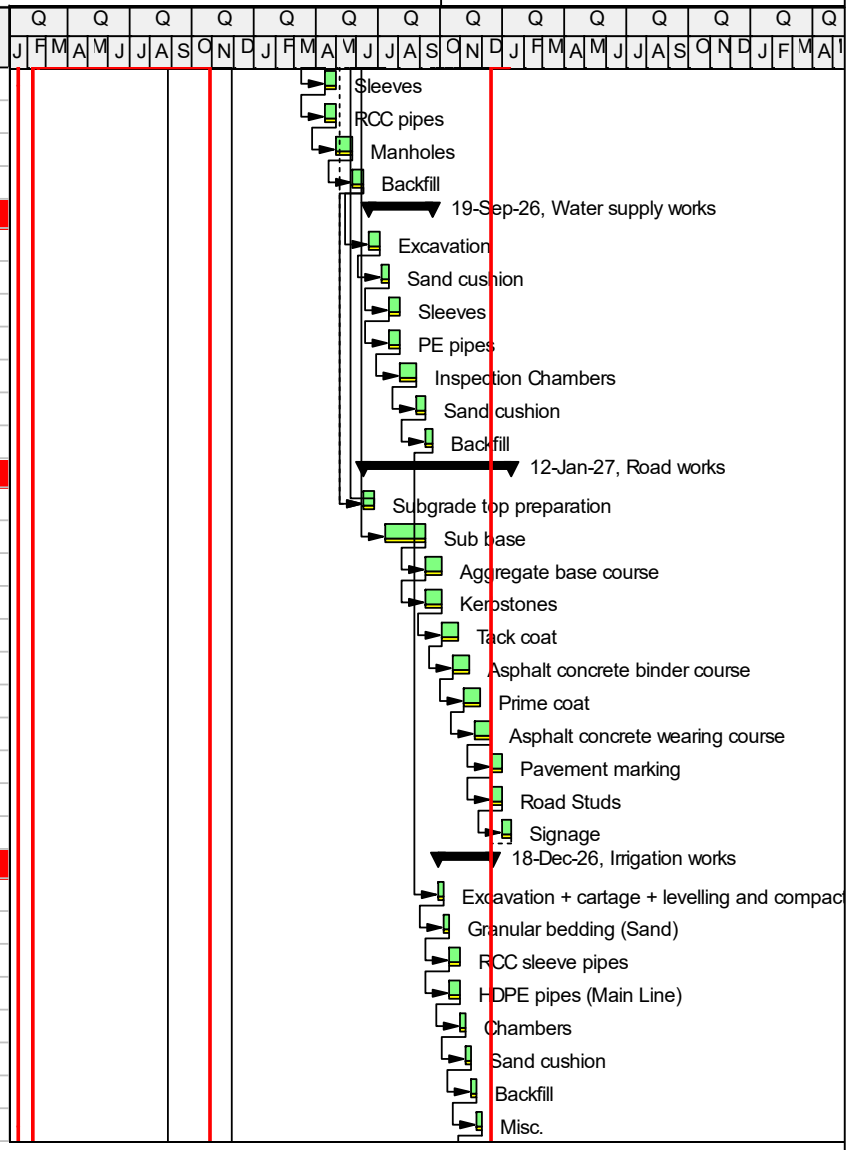

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A53455	PE pipes (Drip Irrigation)	14	03-Dec-26	18-Dec-26
Road 2		577	18-Mar-25	19-Jan-27
Earthwork		319	18-Mar-25	24-Mar-26
A2595	Cutting and removing trees	14	18-Mar-25	02-Apr-25
A2597	CG	14	26-Mar-25	10-Apr-25
A2599	NGC	14	11-Apr-25	26-Apr-25
A51300	Cut and fill	270	28-Apr-25	07-Mar-26
A51310	Subgrade bottom preparation	14	09-Mar-26	24-Mar-26
Drain works		112	25-Mar-26	01-Aug-26
A51320	Excavation	14	25-Mar-26	09-Apr-26
A51330	Stone Soling	10	10-Apr-26	21-Apr-26
A51335	Lean	4	22-Apr-26	25-Apr-26
A51339	RCC Bed	28	27-Apr-26	28-May-26
A51341	RCC Walls	28	29-May-26	30-Jun-26
A51351	RCC Slab	28	01-Jul-26	01-Aug-26
A51361	Catch basin	14	17-Jul-26	01-Aug-26
Sewerage works		70	06-Apr-26	25-Jun-26
A2670	Excavation	14	06-Apr-26	21-Apr-26
A2680	Sand cushion	10	22-Apr-26	02-May-26
A2682	Sleeves	15	04-May-26	20-May-26
A2683	RCC pipes	15	04-May-26	20-May-26
A2684	Manholes	21	21-May-26	13-Jun-26
A2685	Backfill	10	15-Jun-26	25-Jun-26
Water supply works		83	04-Jul-26	08-Oct-26
A3051	Excavation	14	04-Jul-26	20-Jul-26
A3060	Sand cushion	14	21-Jul-26	05-Aug-26
A3065	Sleeves	10	06-Aug-26	17-Aug-26
A3070	PE pipes	10	06-Aug-26	17-Aug-26
A3075	Inspection chamber	21	18-Aug-26	10-Sep-26
A3080	Sand cushion	14	11-Sep-26	26-Sep-26
A3090	Backfill	10	28-Sep-26	08-Oct-26
Road works		174	01-Jul-26	19-Jan-27
A2718	Subgrade top preparation	14	01-Jul-26	16-Jul-26

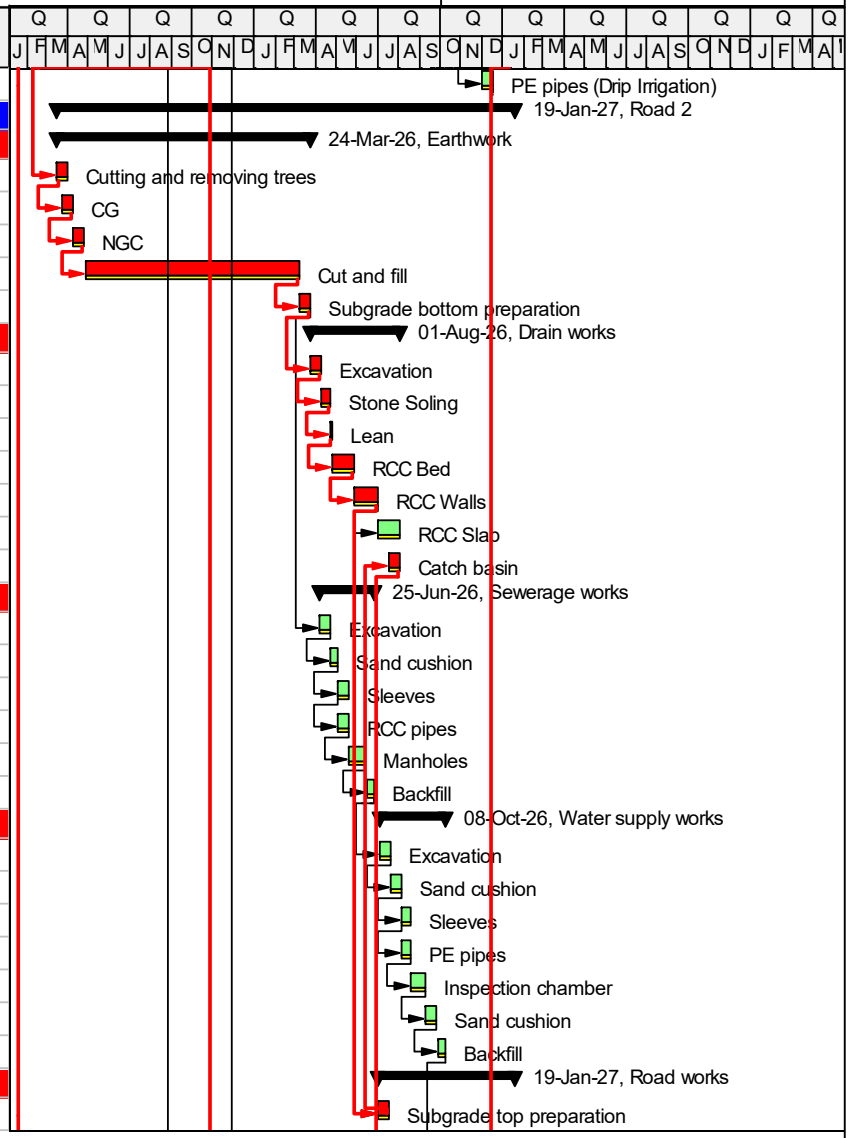

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A2720	Sub base	49	03-Aug-26	28-Sep-26
A2730	Aggregate base course	21	29-Sep-26	22-Oct-26
A2740	Kerbstones	21	29-Sep-26	22-Oct-26
A2750	Tack coat	21	23-Oct-26	16-Nov-26
A2760	Asphalt concrete binder course	21	09-Nov-26	02-Dec-26
A2770	Prime coat	21	25-Nov-26	18-Dec-26
A2780	Asphalt concrete wearing course	21	11-Dec-26	04-Jan-27
A2790	Pavement marking	13	05-Jan-27	19-Jan-27
A2800	Road Studs	13	05-Jan-27	19-Jan-27
A2810	Signage	13	05-Jan-27	19-Jan-27
Irrigation works		70	17-Oct-26	06-Jan-27
A53490	Excavation + cartage + levelling and compact	7	17-Oct-26	24-Oct-26
A53500	Granular bedding (Sand)	7	26-Oct-26	02-Nov-26
A53505	RCC sleeve pipes	14	03-Nov-26	18-Nov-26
A53510	HDPE pipes (Main Line)	14	03-Nov-26	18-Nov-26
A53520	Chambers	7	19-Nov-26	26-Nov-26
A53525	Sand cushion	7	27-Nov-26	04-Dec-26
A53530	Backfill	7	05-Dec-26	12-Dec-26
A53540	Misc.	7	14-Dec-26	21-Dec-26
A53545	PE pipes (Drip Irrigation)	14	22-Dec-26	06-Jan-27
Box Culverts		407	02-Oct-25	19-Jan-27
Three Cell		147	02-Oct-25	21-Mar-26
A51480	Excavation	21	02-Oct-25	25-Oct-25
A51490	Dressing and levelling	10	27-Oct-25	06-Nov-25
A51500	Stone soling	21	07-Nov-25	01-Dec-25
A51510	Lean concrete	4	02-Dec-25	05-Dec-25
A51520	RCC foundation	21	06-Dec-25	30-Dec-25
A51530	RCC walls	28	31-Dec-25	31-Jan-26
A51540	RCC top slab	21	02-Feb-26	25-Feb-26
A51550	Formation of embankment	21	26-Feb-26	21-Mar-26
Two Cell		147	02-Oct-25	21-Mar-26
A51570	Excavation	21	02-Oct-25	25-Oct-25
A51580	Dressing and levelling	10	27-Oct-25	06-Nov-25

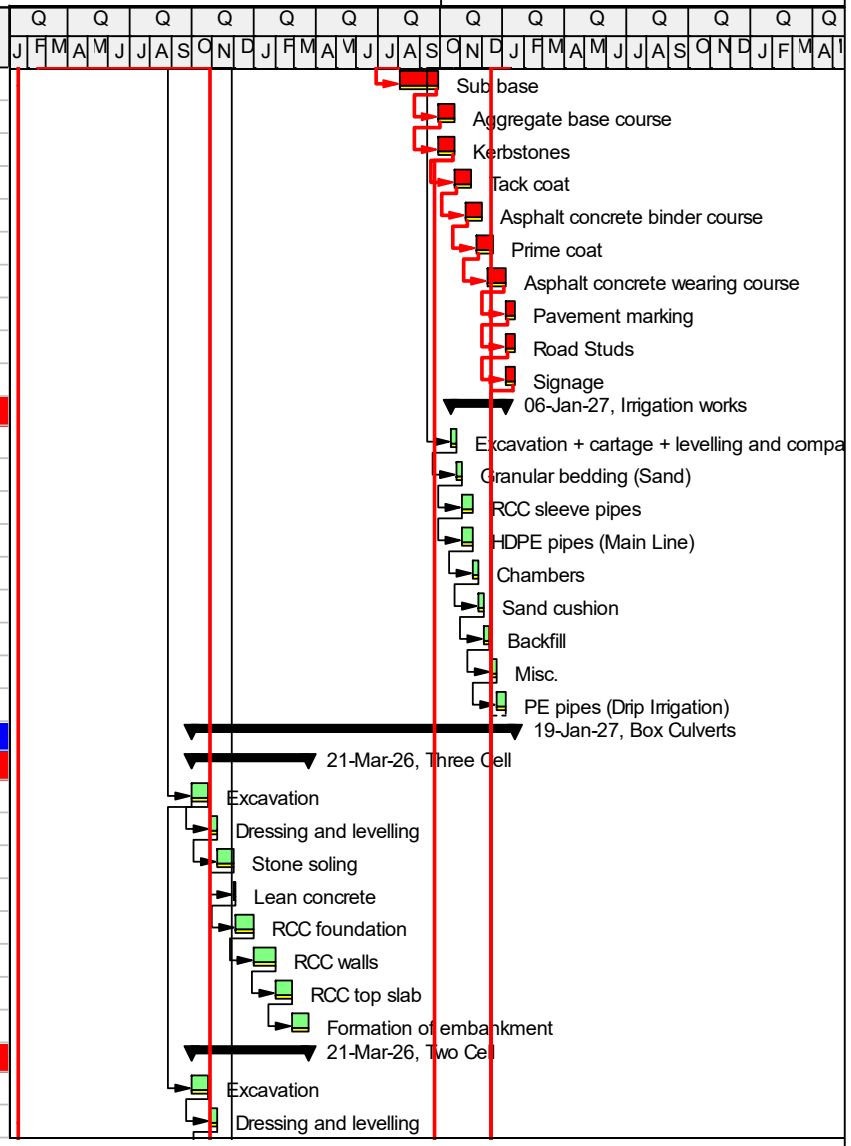

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A51590	Stone soling	21	07-Nov-25	01-Dec-25
A51600	Lean concrete	4	02-Dec-25	05-Dec-25
A51610	RCC foundation	21	06-Dec-25	30-Dec-25
A51620	RCC walls	28	31-Dec-25	31-Jan-26
A51630	RCC top slab	21	02-Feb-26	25-Feb-26
A51640	Formation of embankment	21	26-Feb-26	21-Mar-26
One Cell		**72**	**28-Oct-26**	**19-Jan-27**
A51658	Excavation	7	28-Oct-26	04-Nov-26
A51660	Dressing and levelling	7	05-Nov-26	12-Nov-26
A51670	Stone soling	7	13-Nov-26	20-Nov-26
A51680	Lean concrete	2	21-Nov-26	23-Nov-26
A51690	RCC foundation	14	24-Nov-26	09-Dec-26
A51700	RCC walls	14	10-Dec-26	25-Dec-26
A51710	RCC top slab	14	26-Dec-26	11-Jan-27
A51720	Formation of embankment	7	12-Jan-27	19-Jan-27
Water Supply Bore, Reservoir & Pump Station		**353**	**02-Dec-25**	**16-Jan-27**
Tube well		**63**	**02-Dec-25**	**12-Feb-26**
A52330	Boring	21	02-Dec-25	25-Dec-25
A52340	Screen / Blind pipe (uPVC)	14	26-Dec-25	10-Jan-26
A52345	Shrouding graded bajri	7	12-Jan-26	19-Jan-26
A52350	Pump Riser Pipe	7	20-Jan-26	27-Jan-26
A52360	Misc.	14	28-Jan-26	12-Feb-26
Tube well chamber		**56**	**13-Nov-26**	**16-Jan-27**
A50180	Excavation	14	13-Nov-26	28-Nov-26
A50190	RCC foundation	7	30-Nov-26	07-Dec-26
A50200	RCC walls	14	08-Dec-26	23-Dec-26
A50210	Block masonry	7	24-Dec-26	31-Dec-26
A50220	Plaster	7	01-Jan-27	08-Jan-27
A50230	Water proofing	7	01-Jan-27	08-Jan-27
A50240	Roof Slab	7	01-Jan-27	08-Jan-27
A50260	Misc.	7	09-Jan-27	16-Jan-27
Water Reservoir		**162**	**03-Jan-26**	**10-Jul-26**
A50270	Excavation	21	03-Jan-26	27-Jan-26

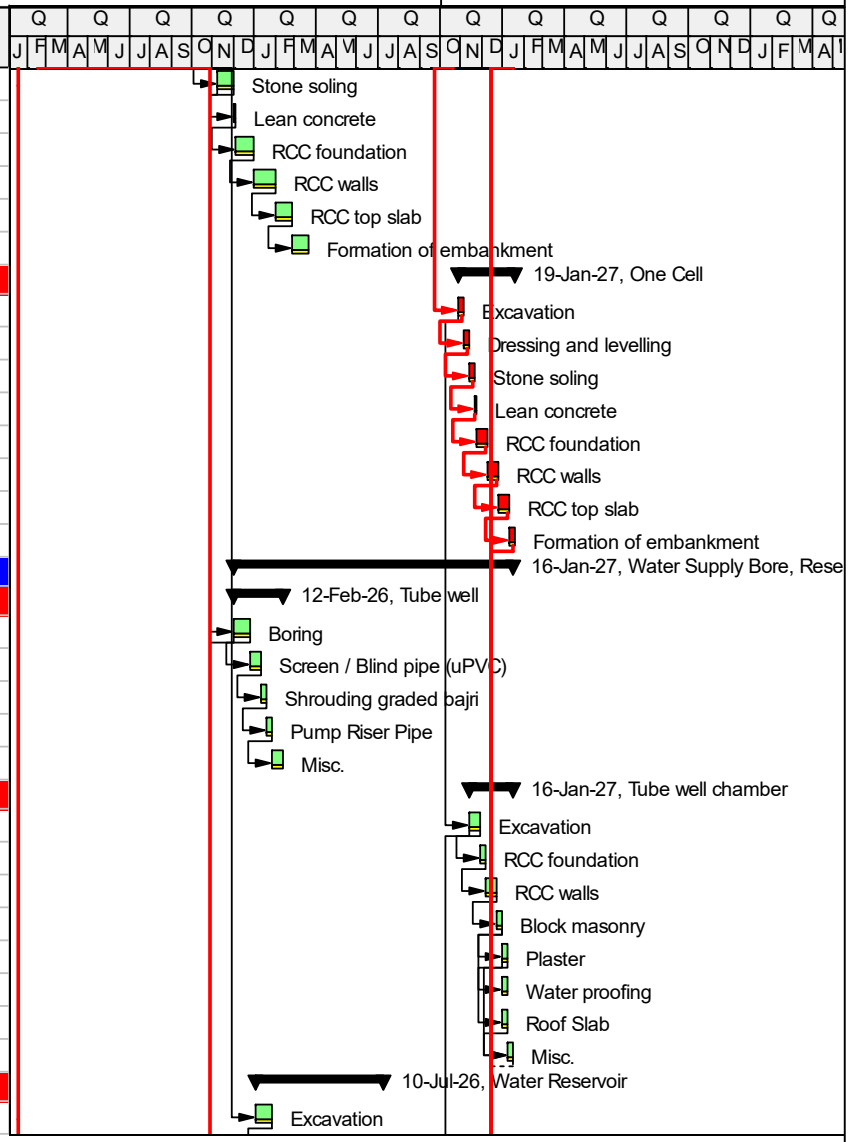

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A50290	Dressing and levelling	14	28-Jan-26	12-Feb-26
A50295	Stone soling	14	13-Feb-26	28-Feb-26
A50300	Lean concrete	4	02-Mar-26	05-Mar-26
A50310	Membrane	7	06-Mar-26	13-Mar-26
A50315	Lean concrete	4	14-Mar-26	18-Mar-26
A50320	RCC foundation	14	19-Mar-26	03-Apr-26
A50340	RCC walls	21	04-Apr-26	28-Apr-26
A50400	RCC columns	21	04-Apr-26	28-Apr-26
A50410	RCC beams	14	29-Apr-26	14-May-26
A50420	RCC top slab	14	15-May-26	30-May-26
A50425	Internal Plaster	7	15-May-26	22-May-26
A50435	External Membrane	7	01-Jun-26	08-Jun-26
A50437	Block Masonry	7	09-Jun-26	16-Jun-26
A50439	Backfill	14	17-Jun-26	02-Jul-26
A50440	Misc.	7	03-Jul-26	10-Jul-26
Pump Station		**84**	**03-Jul-26**	**08-Oct-26**
A50450	Excavation	14	03-Jul-26	18-Jul-26
A50460	Compaction	7	20-Jul-26	27-Jul-26
A50470	Foundation Slab	14	28-Jul-26	12-Aug-26
A50480	Block masonry	14	13-Aug-26	28-Aug-26
A50490	RCC lintel	7	29-Aug-26	05-Sep-26
A50500	RCC Beam	7	07-Sep-26	14-Sep-26
A50510	RCC Roof Sab	7	15-Sep-26	22-Sep-26
A50520	Parapet wall	7	23-Sep-26	30-Sep-26
A50530	Misc.	7	01-Oct-26	08-Oct-26
Irrigation Bore, Reservoir & Pump Station		**353**	**02-Dec-25**	**16-Jan-27**
Tube well		**63**	**02-Dec-25**	**12-Feb-26**
A50570	Boring	21	02-Dec-25	25-Dec-25
A50590	Screen / Blind pipe (uPVC)	14	26-Dec-25	10-Jan-26
A50595	Shrouding graded bajri	7	12-Jan-26	19-Jan-26
A50600	Pump Riser Pipe	7	20-Jan-26	27-Jan-26
A50620	Misc.	14	28-Jan-26	12-Feb-26
Tube well chamber		**56**	**13-Nov-26**	**16-Jan-27**

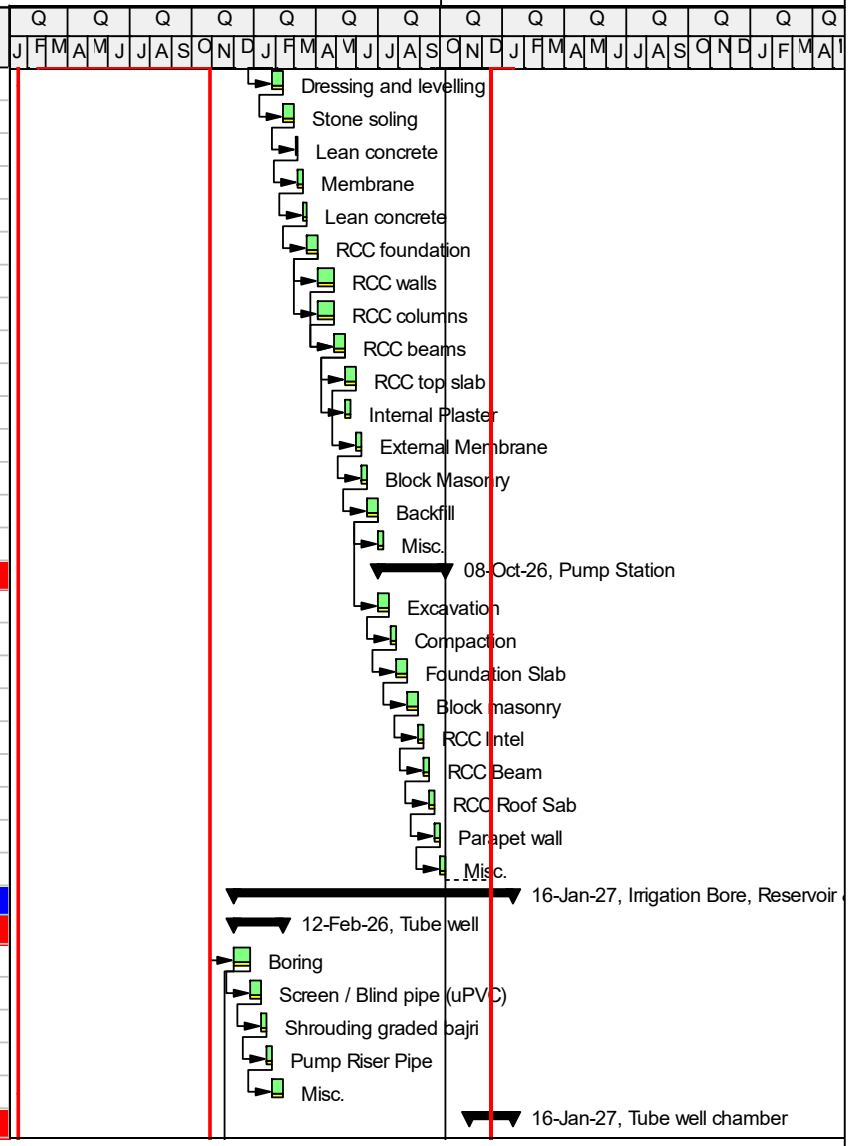

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A52210	Excavation	14	13-Nov-26	28-Nov-26
A52220	RCC foundation	7	30-Nov-26	07-Dec-26
A52230	RCC walls	14	08-Dec-26	23-Dec-26
A52240	Block masonry	7	24-Dec-26	31-Dec-26
A52250	Plaster	7	01-Jan-27	08-Jan-27
A52260	Water proofing	7	09-Jan-27	16-Jan-27
A52270	Roof slab	7	01-Jan-27	08-Jan-27
A52320	Misc.	7	09-Jan-27	16-Jan-27
Irrigation Reservoir		**161**	**23-Dec-25**	**27-Jun-26**
A50730	Excavation	21	23-Dec-25	15-Jan-26
A50740	Dressing and levelling	10	16-Jan-26	27-Jan-26
A50745	Stone soling	14	28-Jan-26	12-Feb-26
A50750	Lean concrete	4	13-Feb-26	17-Feb-26
A50760	Membrane	10	18-Feb-26	28-Feb-26
A50765	Lean concrete	4	02-Mar-26	05-Mar-26
A50770	RCC foundation	14	06-Mar-26	21-Mar-26
A50790	RCC walls	21	23-Mar-26	15-Apr-26
A50800	RCC columns	21	23-Mar-26	15-Apr-26
A50810	RCC beams	14	16-Apr-26	01-May-26
A50820	RCC top slab	14	02-May-26	18-May-26
A50850	Internal Plaster	7	02-May-26	09-May-26
A50860	External Membrane	7	19-May-26	26-May-26
A50870	Block Masonry	7	27-May-26	03-Jun-26
A50880	Backfill	14	04-Jun-26	19-Jun-26
A50990	Misc.	7	20-Jun-26	27-Jun-26
Pump Station		**77**	**20-Jun-26**	**17-Sep-26**
A50900	Foundation Slab	14	20-Jun-26	06-Jul-26
A50910	Block masonry	7	07-Jul-26	14-Jul-26
A50920	RCC lintel	7	15-Jul-26	22-Jul-26
A50930	RCC Beam	14	23-Jul-26	07-Aug-26
A50940	RCC Roof Sab	14	08-Aug-26	24-Aug-26
A50950	Parapet wall	14	25-Aug-26	09-Sep-26
A50960	Misc.	7	10-Sep-26	17-Sep-26

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
Urban Forest		356	01-Dec-25	19-Jan-27
Lake		142	01-Dec-25	14-May-26
A52370	Excavation	21	01-Dec-25	24-Dec-25
A52380	Stone soling	14	25-Dec-25	09-Jan-26
A52390	Lean	7	10-Jan-26	17-Jan-26
A52400	Embankment	21	19-Jan-26	11-Feb-26
A52410	Stone pitching	21	12-Feb-26	07-Mar-26
A52420	Lean	7	09-Mar-26	16-Mar-26
A52430	Membrane	14	17-Mar-26	01-Apr-26
A52440	Lean	7	02-Apr-26	09-Apr-26
A52450	Fibre reinforced concrete	30	10-Apr-26	14-May-26
Island		214	15-May-26	19-Jan-27
A52560	Kerbstones	10	15-May-26	26-May-26
A52570	Crushed stones (Pebbles)	14	27-May-26	11-Jun-26
A52580	Pedestrian Bridges	90	12-Jun-26	24-Sep-26
A52590	Trees	190	12-Jun-26	19-Jan-27
A52600	Misc. (Bush barriers, Precast bench, Sitting bc	190	12-Jun-26	19-Jan-27
Activity Area		214	15-May-26	19-Jan-27
A52465	Compacted Earth	14	15-May-26	30-May-26
A52470	Kerbstones	10	01-Jun-26	11-Jun-26
A52480	Crushed stones (Pebbles)	14	12-Jun-26	27-Jun-26
A52490	Palm Trees	184	19-Jun-26	19-Jan-27
A52500	Misc. (Precast bench, Sitting bollard, Stepping	184	19-Jun-26	19-Jan-27
Bicycle Track		214	15-May-26	19-Jan-27
A52505	Compacted Earth	14	15-May-26	30-May-26
A52510	Kerbstones	10	01-Jun-26	11-Jun-26
A52520	Murrum soil	20	12-Jun-26	04-Jul-26
A52530	Ground cover / Shrubs	170	06-Jul-26	19-Jan-27
A52540	Misc.	170	06-Jul-26	19-Jan-27
Guard Room and Toilet Block		356	01-Dec-25	19-Jan-27
A52620	Substructure	90	01-Dec-25	14-Mar-26
A52630	Superstructure	120	16-Mar-26	01-Aug-26
A52635	OHWT	90	03-Aug-26	14-Nov-26

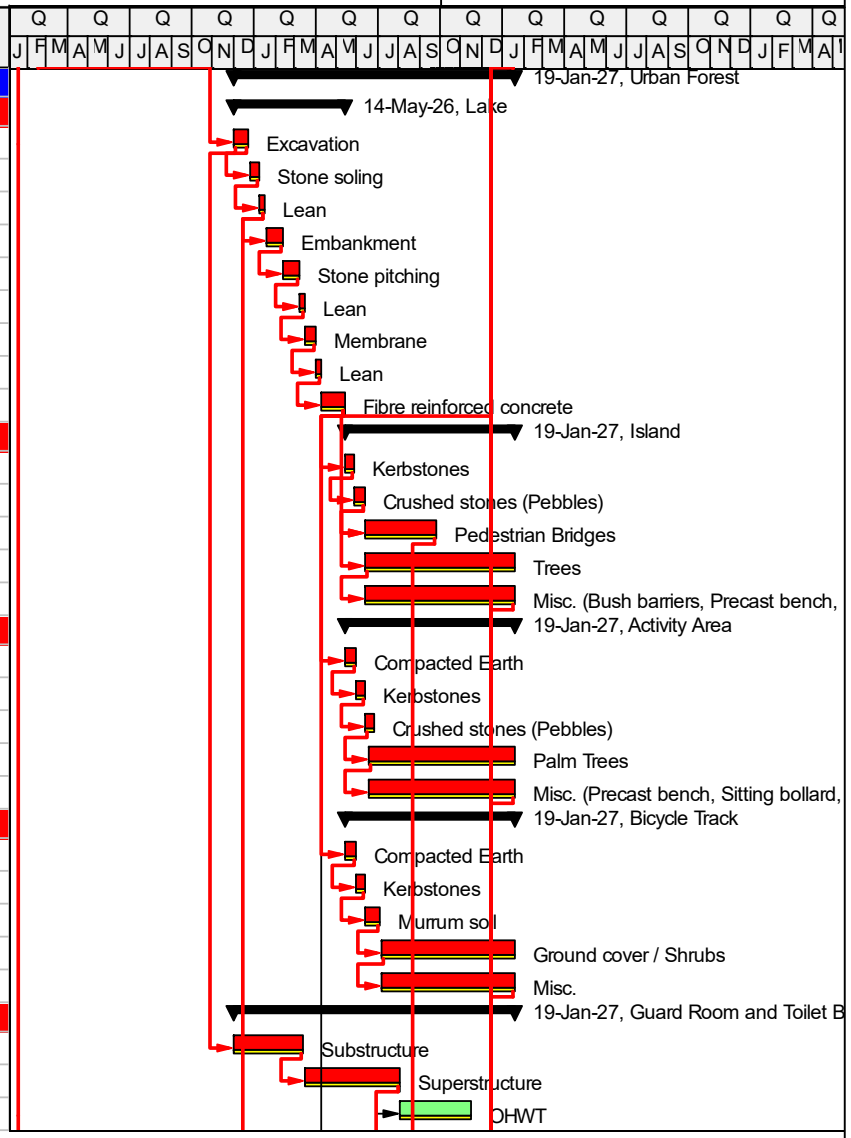

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

REVISED SCHEDULE	INFRASTRUCTURE DEVELOPMENT OF EDUCATION CITY, KARACHI PHASE 1	EXCLUDING BRIDGE AND GATE HOUSE

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A52640	Architecture works (wall + floor + ceiling finishe	146	03-Aug-26	19-Jan-27
Miyawaki Forest		314	19-Jan-26	19-Jan-27
A52545	Rough dressing of the area	42	19-Jan-26	07-Mar-26
A52547	Pits	268	09-Mar-26	14-Jan-27
A52549	Supplying and stacking approved garden soil	268	10-Mar-26	15-Jan-27
A52553	Supplying, stacking and spreading cow dung	268	11-Mar-26	16-Jan-27
A52555	Supplying and stacking live (Bermuda) grass i	268	12-Mar-26	18-Jan-27
A52557	Providing and planting Miyawaki Forest area c	268	13-Mar-26	19-Jan-27
Fruit Orchard / Farming Land		314	19-Jan-26	19-Jan-27
A54020	Compacted Earth	42	19-Jan-26	07-Mar-26
A54030	Trees	268	13-Mar-26	19-Jan-27
Entrance		100	25-Sep-26	19-Jan-27
A53975	Compacted Earth	3	25-Sep-26	28-Sep-26
A53980	Crushed stone (Pebbles)	7	29-Sep-26	06-Oct-26
A53990	Stepping Stones	7	29-Sep-26	06-Oct-26
A54010	Trees	90	07-Oct-26	19-Jan-27
BBQ Area		100	25-Sep-26	19-Jan-27
A53940	Compacted Earth	3	25-Sep-26	28-Sep-26
A53945	Kerbstones	7	29-Sep-26	06-Oct-26
A53950	Crushed stones (Pebbles)	7	29-Sep-26	06-Oct-26
A53970	Misc. (Precast bench, Sitting bollard, Boulders	90	07-Oct-26	19-Jan-27
Electrical Works		20	28-Dec-26	19-Jan-27
A4171	uPVC class D pipe	7	28-Dec-26	04-Jan-27
A4172	PVC cables	7	05-Jan-27	12-Jan-27
A4174	DB	6	13-Jan-27	19-Jan-27
A4180	LED Light Pole	6	13-Jan-27	19-Jan-27
A4310	Power Manhole	6	13-Jan-27	19-Jan-27
A4320	Misc. (Isolators, Pull box)	6	13-Jan-27	19-Jan-27
Stream		214	15-May-26	19-Jan-27
Civil Works		148	15-May-26	03-Nov-26
A3640	Excavation	21	15-May-26	08-Jun-26
A3650	Stone soling	14	09-Jun-26	24-Jun-26
A3655	Lean	7	25-Jun-26	02-Jul-26
A3665	Embankment	21	03-Jul-26	27-Jul-26

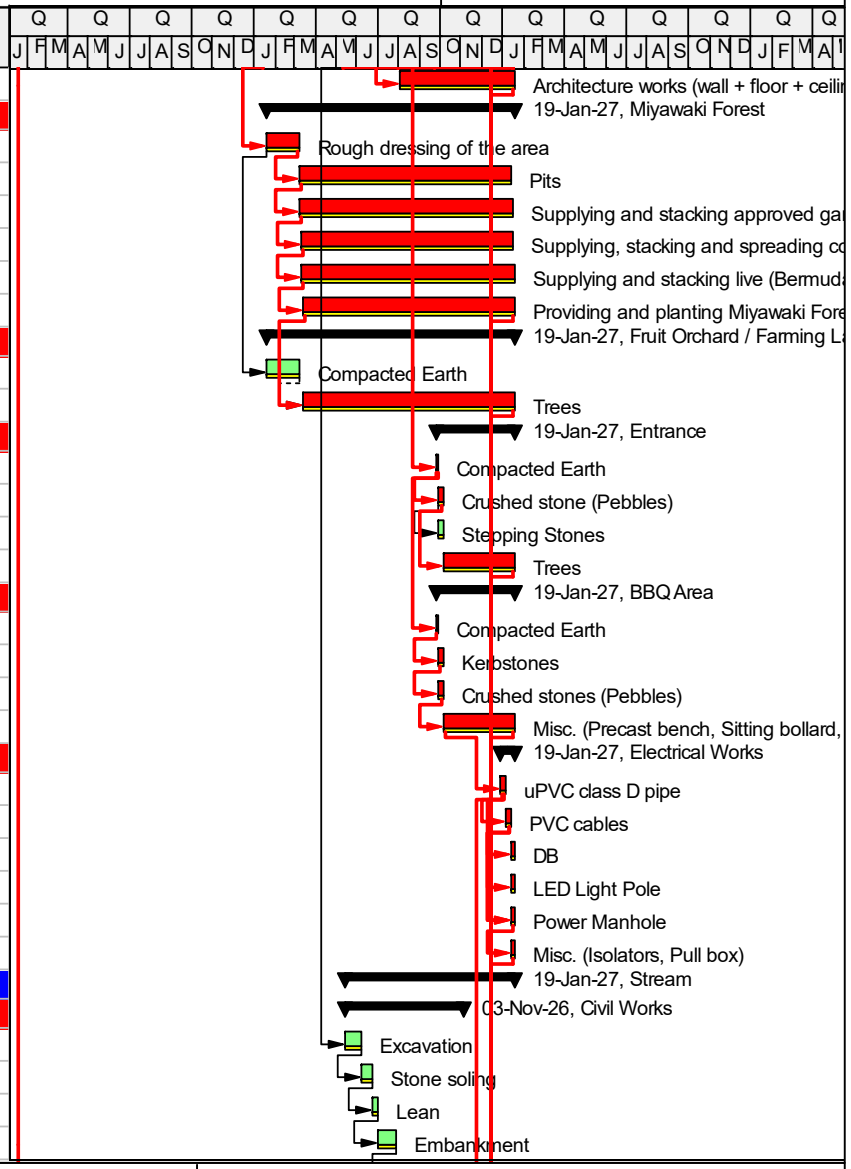

Project Baseline Bar | Remaining Work | Actual Work | Critical Remaining Work

© Oracle Corporation

Activity ID	Activity Name	Original Duration	BL Project Start	BL Project Finish
A3675	Stone pitching	21	28-Jul-26	20-Aug-26
A3685	Lean	10	21-Aug-26	01-Sep-26
A3695	Membrane	14	02-Sep-26	17-Sep-26
A3705	Lean	10	18-Sep-26	29-Sep-26
A3715	Fibre reinforced concrete	30	30-Sep-26	03-Nov-26
Electrical Works		20	28-Dec-26	19-Jan-27
A3838	uPVC class D pipe	7	28-Dec-26	04-Jan-27
A3839	PVC cables	7	05-Jan-27	12-Jan-27
A3840	DB	6	13-Jan-27	19-Jan-27
A3846	LED Light Pole	6	13-Jan-27	19-Jan-27
A3890	Power Manhole	6	13-Jan-27	19-Jan-27
A3900	Misc. (Isolators, Pull box)	6	13-Jan-27	19-Jan-27
Handing Over		0	19-Jan-27	19-Jan-27
A50060	Handing over and taking over	0		19-Jan-27

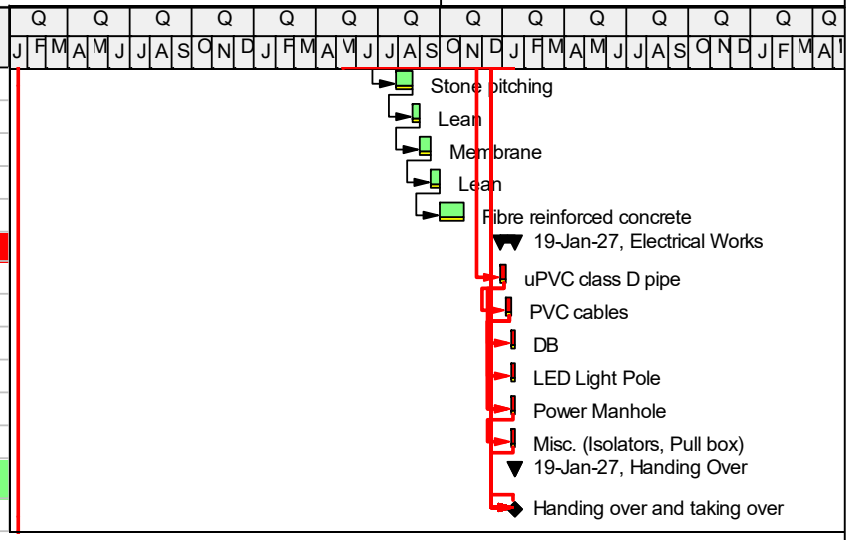

Project Baseline Bar | Remaining Work
Actual Work | Critical Remaining Work

© Oracle Corporation
